SDEM® 2.0 Getting Started Guide

Japan Global Gateway

FUJITSU-RESTRICTED

[September 01, 2022]

Copyright 2022 FUJITSU LIMITED

This training course is intended for those who selected "SDEM 2.0 Getting Started Guide," for those not familiar with SDEM including the old SDEM, in the SDEM 2.0 Introductory Training.

Contents - SDEM Getting Started Guide -

FUJITSU

1. What is SDEM?
   1.1 Need for Standardization
   1.2 Fujitsu Standardization = Standard Process Structure "SDEM"
   1.3 Support for Global/De Facto Standards
   1.4 History of Standardization at Fujitsu

2. SDEM Structure
   2.1 SDEM Processes
   2.2 Process Structure
   2.3 Categories
   2.4 Phases
   2.5 WBS (Work Breakdown Structure)

Copyright 2022 FUJITSU LIMITED

Copyright 2022 FUJITSU LIMITED

Contents - SDEM Getting Started Guide -

FUJITSU

3. Each SDEM Process
3.1 Planning Process
3.2 Requirement Definition/Development/Operational Test & Transition Process
3.2.1 Requirement Definition/Development/Operational Test & Transition Process Categories
3.2.2 Requirement Definition Process
3.2.3 Development Process
3.2.4 Operational Test & Transition Process
3.2.5 Main WBS Flow of Requirement Definition/Development/Operational Test & Transition Process
3.3 Operation & Maintenance Process

4. SDEM 2.0 Content Structure
4.1 Overall SDEM Structure
4.2 SDEM Standard Processes
4.3 Structure of SDEM Practical Standards

Copyright 2022 FUJITSU LIMITED

Copyright 2022 FUJITSU LIMITED

Contents - SDEM Getting Started Guide -

FUJITSU

5. Applying SDEM
   5.1 Applying SDEM to Projects
   5.2 Concept of Tailoring
   5.3 Concept of Utilizing SDEM in Agile Development

6. SDEM Usage Scenarios
   6.1 Use SDEM at These Times
   6.2 SDEM Usage Scenario 1) Planning Project Plan Scheme and Role Division
   6.3 SDEM Usage Scenario 2) Creating Schedule
   6.4 Scope of SDEM 2.0 Provision
   6.5 SDEM 2.0 Published by IKB-SDEM

Copyright 2022 FUJITSU LIMITED

Copyright 2022 FUJITSU LIMITED

FUJITSU

1. What is SDEM?

What you will understand by the end of this chapter

- Why standardization is required in system development
- What is SDEM, Fujitsu's standard process structure

Copyright 2022 FUJITSU LIMITED

Chapter 1 explains what SDEM is.
By the end of this chapter, you will understand why standardization is required in system development and what is SDEM, Fujitsu's standard processes.

Copyright 2022 FUJITSU LIMITED

1.1 Need for Standardization - Why Standardization is Required - FUJITSU

To build quality, the processes for planning, design, implementation, and testing must be done **in the correct order**.

To provide customers with systems they can use with peace of mind, an architecture for work **at the same quality by many parties** is required.

Standardization

Copyright 2022 FUJITSU LIMITED

First is an explanation of why standardization is required in system development, operation, and maintenance.

To create high quality in systems, the processes for planning, design, implementation, and testing must be done in the correct order.
In addition, to provide customers with systems they can use with peace of mind, an architecture for work at the same quality by many parties is required.
The standardization of processes and the development architecture allows many parties to work at the same quality in the correct order.

Examples of standardization are:
- "standard processes" that define work contents and procedures, and
- "standard documents" that define the formats and rules of design, management, and other documents.

Copyright 2022 FUJITSU LIMITED

1.1 Need for Standardization - Non-Standardized State -

FUJITSU

Quality varies depending on the person

Work that should be done and descriptions in documents are omitted

Interfaces are incoherent and do not work well together

Maintainability is not good at the time of design change or repair after operation

Copyright 2022 FUJITSU LIMITED

So what kind of problems occur when processes and documents are not standardized?

For example, the following problems occur:
- Quality varies depending on the person
- Work that should be done is omitted
- Interfaces are incoherent and do not work well together

To prevent such problems, the required work and deliverables must be clarified. Standardization, that is, the processes and architecture in place, is important to ensure that the required work is carried out properly, even by those without experience.

Copyright 2022 FUJITSU LIMITED

1.1 Need for Standardization - Effects of Standardization -

FUJITSU

Effect 1 Work and quality are independent of people

Effect 2 Even inexperienced members understand the correct procedures for manufacturing with good quality

Effect 3 Information can be accurately transmitted without omission to the people in each role

Effect 4 Maintainability during operation and maintenance is improved by the handover of documents that comply with development standards

Copyright 2022 FUJITSU LIMITED

Various effects can be expected from standardization.

Firstly, when the documents created with the standard documents, the items written in them, and the required work are defined, you can prevent a dependence on the individual in work and quality.

Secondly, when the required work and its procedures are shown as standard processes, even inexperienced members can carry out manufacturing in the correct order.

Thirdly, when the role division and required work in standard processes are clarified, you can convey information accurately and without omission and unify how it is understood by the parties concerned.

Fourthly, after documents created using standard documents are handed over for operation and maintenance, everyone understands what is written and where it is, which improves maintainability.

The next page explains what kind of standardization is underway at Fujitsu.

Copyright 2022 FUJITSU LIMITED

1.2 Fujitsu Standardization = Standard Process Structure "SDEM"

FUJITSU

Fujitsu's standard process structure "SDEM"

- Systematizes the basic concepts and elements of planning, development, operation and maintenance, and quality assurance activities in Fujitsu's system development as standard processes
- Comprehensively systematizes the who, what, when, and what order of work to prevent omissions and ensure quality
- Gives a bird's-eye view of the whole like a map so that users understand their positions in it and communicate in a common language with the parties concerned

Copyright 2022 FUJITSU LIMITED

Fujitsu's standard process structure is called "SDEM."

It shows the basic concepts of planning, development, operation and maintenance, and quality assurance activities for systems handled by Fujitsu.

It is a bible for comprehensively systematizing the who, what, when, and what order of work to prevent omissions and ensure quality.

By using SDEM, you can get a bird's-eye view of the whole like a map and understand your position in it. So you will be able to communicate in a common language with the parties concerned.

Copyright 2022 FUJITSU LIMITED

1.3 Support for Global/De Facto Standards

FUJITSU

Systematization based on global/de facto standards such as ISO/IEC/JIS, Common Frame, PMBOK, and ITIL, and Fujitsu's practical know-how

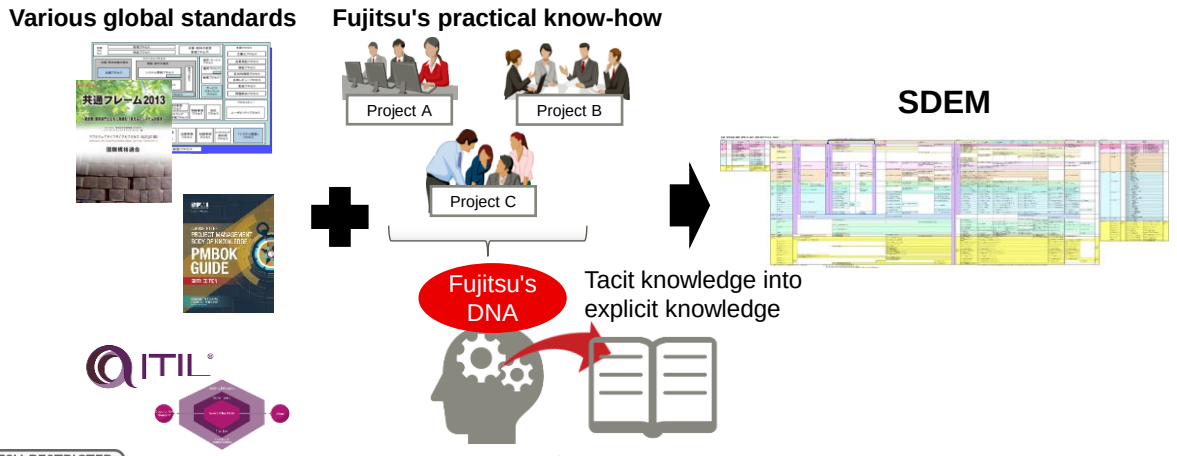

Copyright 2022 FUJITSU LIMITED

SDEM has been systematized by incorporating various domestic and global standards, such as Common Frame and ITIL, in addition to Fujitsu's conventional practical know-how.

As a result, it can be used for projects that require compliance with global standards.

Copyright 2022 FUJITSU LIMITED

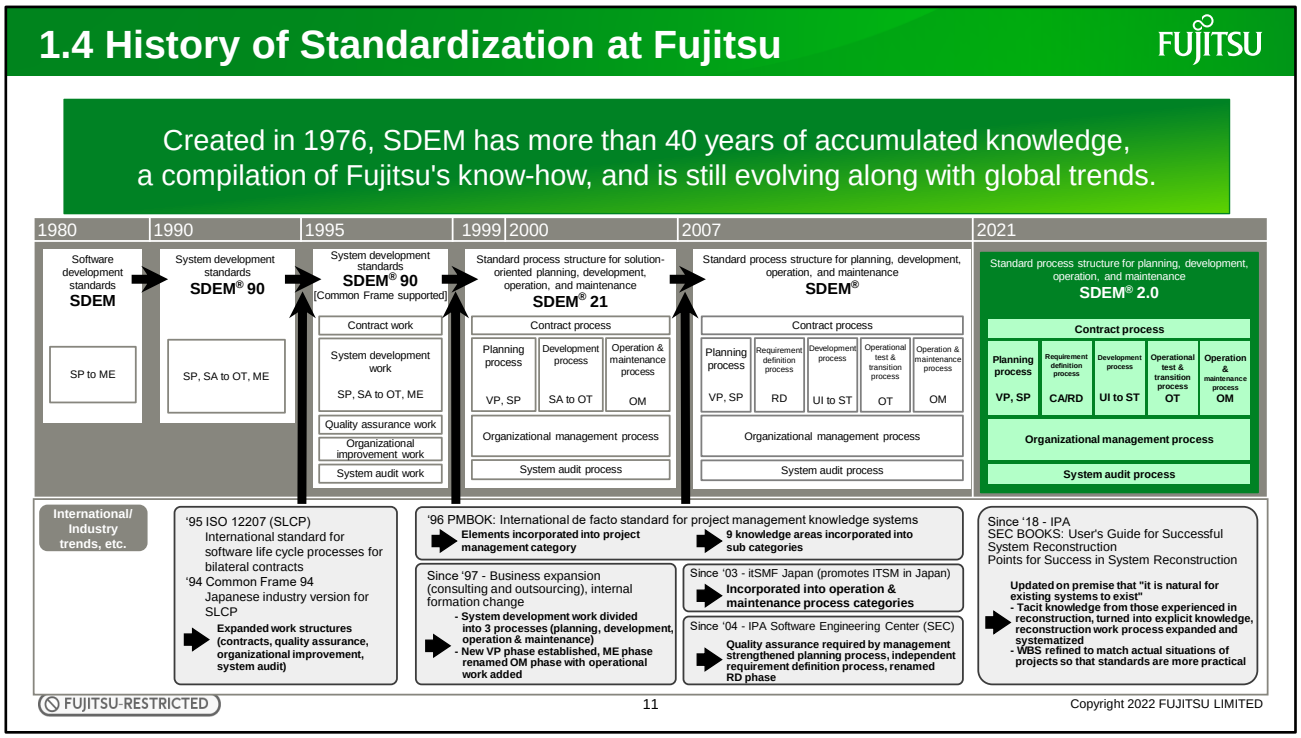

Fujitsu's SDEM has more than 40 years of accumulated knowledge, which continues to be used in the field as a compilation of Fujitsu's know-how.

Here is a brief explanation about its history.

SDEM was born in 1976.
The purposes were to break away from development practices that depend on individual skills, and to curb the ever-increasing development costs.

In 1995, SDEM supported the common framework established as an industry standard in Japan. At the time, not only system development but also contract and organizational work was added, creating a prototype for the current SDEM processes.

Since then, SDEM has continued to incorporate elements of international and de facto standards, responding to changes in the environment surrounding system construction.

In 2021, it was reformed into SDEM 2.0.
The main theme of SDEM up to then was "creating a new system."
However, it is now commonplace to have an existing system.
Therefore, SDEM was updated on the premise that "it is natural for existing system to exist."

SDEM will continue to evolve in the future.

Copyright 2022 FUJITSU LIMITED

2. SDEM Structure

What you will understand by the end of this chapter

- What are SDEM categories, phases, and WBS

Copyright 2022 FUJITSU LIMITED

Chapter 2 explains the SDEM structure.
By the end of this chapter, you will understand the SDEM categories, phases, and WBS.

Copyright 2022 FUJITSU LIMITED

2.1 SDEM Processes

FUJITSU

SDEM is systemization dividing system planning, development, and operation and maintenance into 8 processes.

[Project processes]

Contract process
Engage in contract work between purchaser and supplier

Planning process	Requirement definition process	Development process	Operational test & transition process	Operation & maintenance process
Formulate IT strategy closely aligned with management strategy	Confirm requests from users, etc. to system based on IT strategy, and define system requirements as inputs for system development	Efficiently and reliably realize system requirements as system	Use system created in development process for users' operational tests, production decisions, and migration to new business/system	Maintain, evaluate, and improve system so that users can smoothly carry out their duties

[Organizational processes]

Organizational management process
Manage organization to efficiently and effectively support projects to achieve organizational goals

System audit process
A system auditor independent of the audit target evaluates whether or not IT system-related risks are properly controlled. * In Japan, the system audit process is based on the system audit standards, system management standards, and so on established by the Ministry of Economy, Trade and Industry. SDEM does not specify the contents of the process.

* This training course explains the processes from planning to operation & maintenance. For the contract, organizational management, and system audit processes, see the *Standard Process Guide* for SDEM 2.0.

Copyright 2022 FUJITSU LIMITED

First is an explanation of the SDEM process structure.

The SDEM processes are broadly divided into project processes and organizational processes.
The project processes consist of processes for the system life cycle and the contract process. The processes for the system life cycle consist of five processes: planning, requirement definition, development, operational test & transition, and operation & maintenance.
The organizational processes are processes handled by the organization to support a project, and they consist of the organizational management process and system audit process.

This training course explains the processes from planning to operation & maintenance, which are related to the system life cycle.
For the contract, organizational management, and system audit processes, see the *Standard Process Guide* for SDEM 2.0.
Chapter 4 introduces the *Standard Process Guide*.

Copyright 2022 FUJITSU LIMITED

2.2 Process Structure

FUJITSU

Systematization of "work to be done" along 2 axes: Vertical axis = Categories, Horizontal axis = Phases

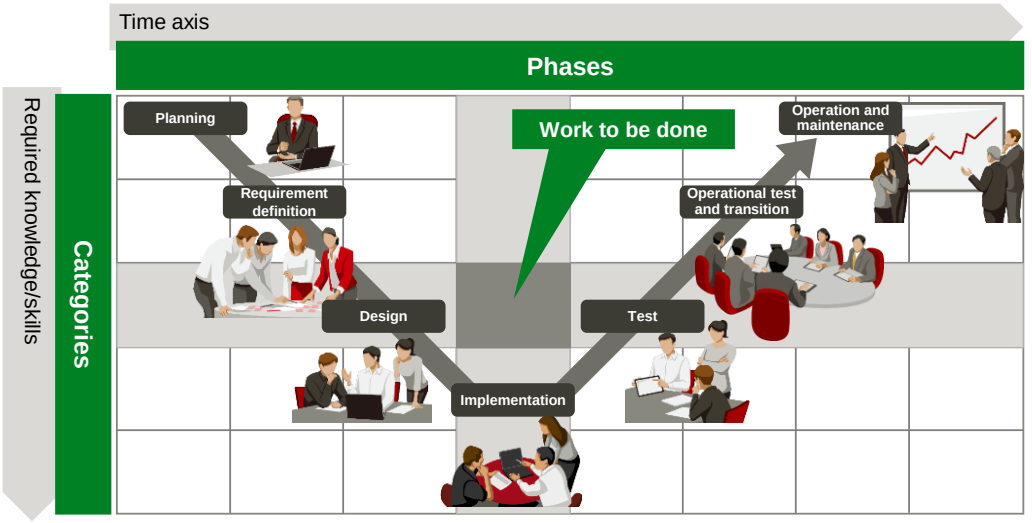

Copyright 2022 FUJITSU LIMITED

Here is an explanation of the structure of the SDEM processes.

The SDEM structure is a matrix with two axes: categories on the vertical axis, and phases on the horizontal axis.
The vertical axis shows the "required knowledge/skills" categories, and the horizontal axis shows the phases, which are the time axis.
"Work to be done" is defined at the intersection.

The vertical axis clarifies "who," the horizontal axis clarifies "when," and the intersection clarifies "what."

The subsequent pages explain the vertical axis "Categories" first, the horizontal axis "Phases" next, and "work to be done" finally.

Copyright 2022 FUJITSU LIMITED

2.3 Categories - Categories in Each Process -

FUJITSU

Categories defined for each process

- Main categories of the work required to carry out each process
- Categories based on work relevance and the relevance of knowledge/skills required for work

Planning process

A: Business management
B: Business
C: System usage
D: System
E: Project management

Requirement definition process
Development process
Operational test & transition process

A: Business management
T: Quality assurance (Overall test)
B: Business
C: System requirements
D: Application
E: Application infrastructure
F: System infrastructure
G: Operation and maintenance
H: Transition & deployment
I: Development support
J: Project management

Operation & maintenance process

A: Business management
B: Business
C: IT service management
D: System operation and maintenance
E: Infrastructure provision
G: Project management

Copyright 2022 FUJITSU LIMITED

First is an explanation of the Categories vertical axis.

There are the main categories of work required to carry out each process. The categories are based on work relevance and the relevance of knowledge/skills required for work.
Therefore, they can be useful for teaming in a project, as an example.

The categories have been appropriately defined based on the characteristics of the planning process, the requirement definition, development, operational test & transition processes, and the operation & maintenance process.

Copyright 2022 FUJITSU LIMITED

2.3 Categories - System as Combination of Many Technologies -

FUJITSU

A system is a combination of many technologies.

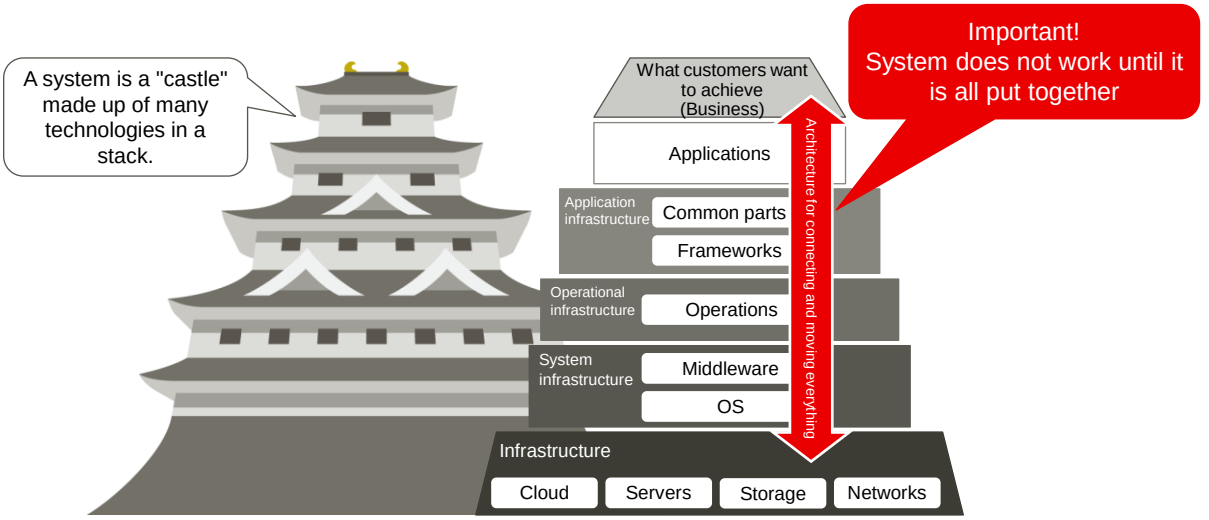

Copyright 2022 FUJITSU LIMITED

Starting with this page, here is a further explanation of the categories in the requirement definition, development, operational test & transition processes, which are the processes of system construction.

First of all, as a premise, a system is made up like this castle with many technologies in a stack. Be aware that an architecture for connecting and moving everything is important, and that the system does not work until it is all put together.

Copyright 2022 FUJITSU LIMITED

2.3 Categories - Correspondence Between System and Categories -

FUJITSU

SDEM categories corresponding to the system structure

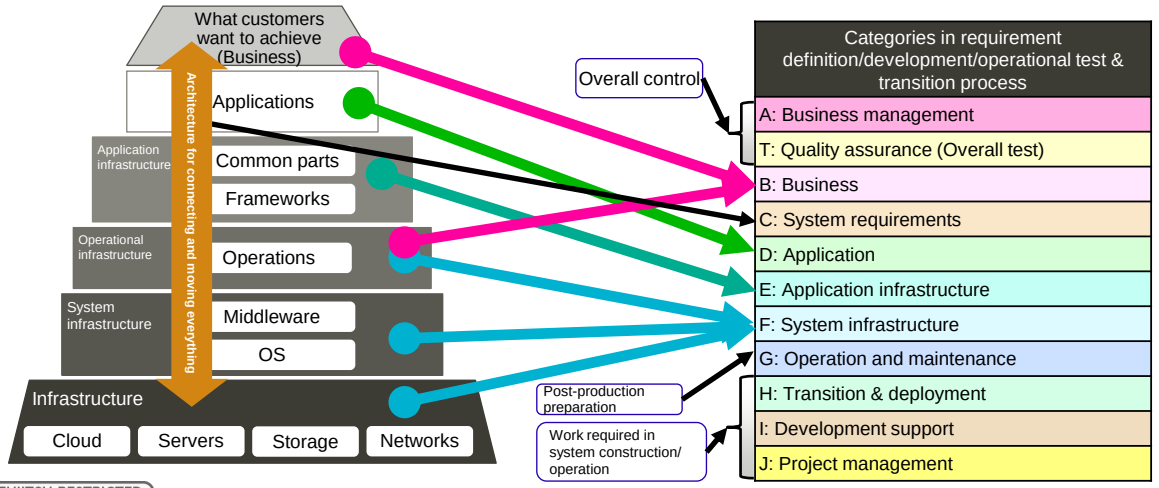

Copyright 2022 FUJITSU LIMITED

The system structure corresponds to the categories in the requirement definition, development, and operational test & transition processes.

One category corresponds to "what customers want to achieve" and others correspond to "work required in system construction/operation" as roles required for system construction. There are other categories as well corresponding to parts of the system structure.

Each category is classified by adding an alphabet letter; for example, "A: Business management" and "B: Business."

Chapter 3 explains the contents of each category.

Copyright 2022 FUJITSU LIMITED

2.4 Phases - Time Divisions in System Life Cycle -

FUJITSU

"Work to be done" by stakeholders involved in the system, mapped to the time axis of system construction
Time period in the system life cycle, and **unit for verifying a series of activities in system development**

- Phases in each process

Time axis

Process	Planning process		Requirement definition process		Development process							Operational test & transition process	Operation & maintenance process
Main phase	Planning		Requirement definition		Design		Implementation			Test		Operational test and transition	Operation and maintenance
Phase	IT vision planning	System planning	Current business and system analysis	System requirement definition	User interface design	System structure design	Program structure design	Programming	Program test	Integration Test	System test	Operational test and transition	Operation and maintenance
Abbreviation	VP	SP	CA	RD	UI	SS	PS	PG	PT	IT	ST	OT	OM

Copyright 2022 FUJITSU LIMITED

Next is about the phases.
The SDEM phases are "work to be done" by stakeholders, such as our customers and us, and they are mapped to the time axis of system construction.

They are time divisions throughout the life cycle of such a system, from planning, requirement definition, design, implementation, test, and operational test and transition to operation and maintenance. They are also units for verifying the progress and quality of the work in system development.

Memorize the abbreviations at the bottom of this table because they are often used to represent the phases.

Copyright 2022 FUJITSU LIMITED

2.4 Phases - V-shaped Model for Quality Assurance in System Development -

FUJITSU

- Entire development process
  - Provide quality assurance by gradually decomposing and creating system components, and gradually integrating and verify them in testing
  - Match the system components at the requirement definition/design stage and the test stage, and verify and confirm quality with the V-shape (V-shaped model for quality assurance)

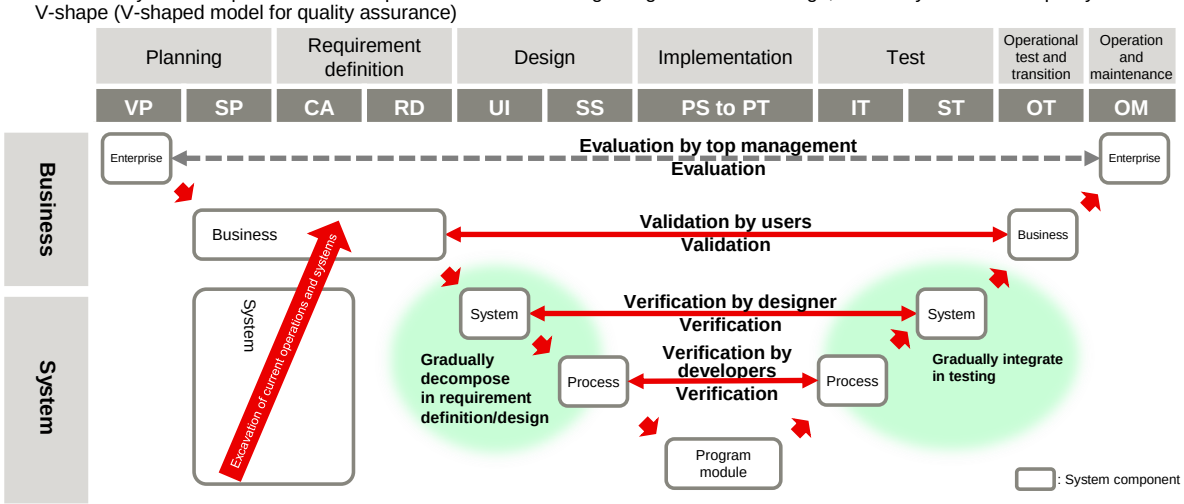

Copyright 2022 FUJITSU LIMITED

Here is an explanation of how the entire development process is systematized.

In SDEM, as the requirement definition, design, and implementation phases progress, the target system components are gradually refined and decomposed in the order of business, system, process, and program. In the test phase, the decomposed system components are integrated in the reverse order of process, system, and business for verification.

Then, those same components are matched and verified in opposing phases for quality assurance.
For example, in the ST phase test, verify that the system is as designed in the UI phase. In the OT phase test, the user validates that the requirements defined for business in the RD phase are satisfied.

This is the concept of the V-shaped model for quality assurance.

Copyright 2022 FUJITSU LIMITED

2.5 WBS (Work Breakdown Structure) - What is WBS? -

FUJITSU

Hierarchization of "work to be done" in 3 stages

	WBS1 level	WBS2 level	WBS3 level
	[Systematization] Most comprehensive project management	**[Refinement] Input units of development resources Role units of project members**	**[Substantiation] Units of deliverables created**
WBS code structure	Sub category*1 + phase*2 + serial number*3 + 00	Level-1 code + serial number*3 + 0	Level-2 code + serial number*3
File structure	Unit of standard filing for categories and phases	Unit that bundles documents for WBS2 level	Output for WBS3 level
File code structure	Level-1 code + f + serial number*3	Level-2 code + t + serial number*3	Level-3 code + d + serial number*3

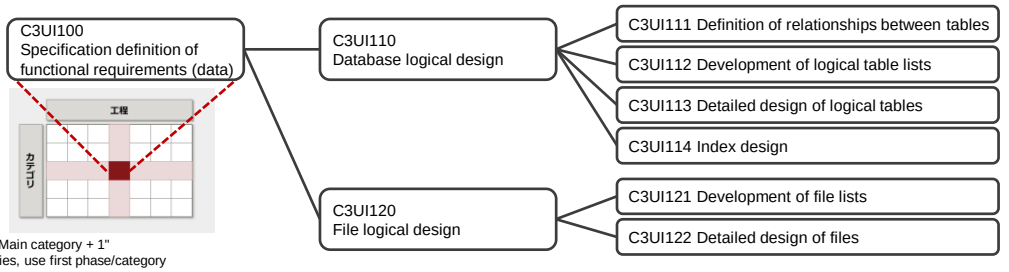

*1 If no sub category, use "Main category + 1"
*2 If across phases/categories, use first phase/category
*3 1 to 9. Thereafter, A to Z

Copyright 2022 FUJITSU LIMITED

Here is an explanation of WBS.

"WBS" stands for Work Breakdown Structure, which is the structure of "work to be done" for each phase and category.
SDEM hierarchizes it in three stages.

The WBS1 level is the systematization level, which provides an overall picture for comprehensive project management.

The WBS2 level is the refinement level, which refines the WBS1 work as the role units of project members.
The work here is also a unit for drawing up a detailed project schedule.

The WBS3 level is a more specific version of work at the WBS2 level.
Basically, the work here is a unit for creating deliverables.

The WBS of each layer is represented by assigned WBS codes indicating a category and phase.

Copyright 2022 FUJITSU LIMITED

2.5 WBS - Extended WBS Across Categories -

FUJITSU

"Z" indicates work requiring consideration from an overall perspective across categories.

In system development, **some work needs consideration from an overall perspective across SDEM categories**.

"Z" is used in the IDs of items requiring consideration across categories.

Example 1:

Z1CA200 Confirmation of reconstruction requests and tentative definition of reconstruction pattern from requests perspective

Requiring consideration from an overall perspective across all categories

Example 2:

DZCA100 Overall understanding of current assets

Requiring consideration across sub categories in Category D

[List of CA phase work items (WBS1)]

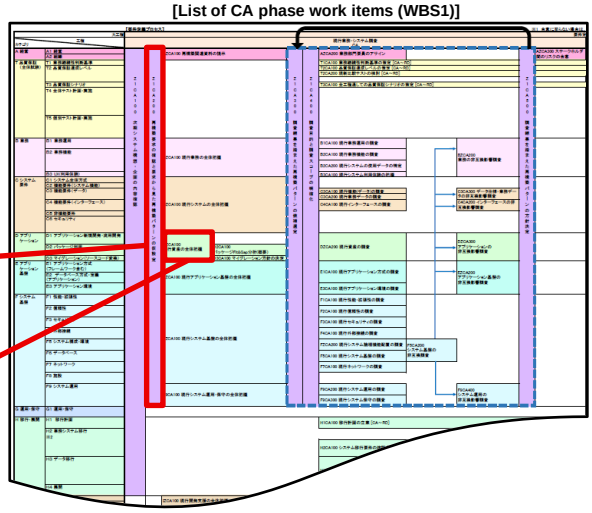

Copyright 2022 FUJITSU LIMITED

In system development, some work needs consideration from an overall perspective across SDEM categories.

For that work, the letter "Z" is used in the category part of the WBS code.

Copyright 2022 FUJITSU LIMITED

FUJITSU

3. Each SDEM Process

What you will understand by the end of this chapter

- Definition and workflow of every phase in each SDEM process
- Role of each category of the SDEM requirement definition/development/operational test & transition process

Copyright 2022 FUJITSU LIMITED

Chapter 3 explains each SDEM process.
By the end of this chapter, you will understand the definition and workflow of each phase, and the role of each category.

Copyright 2022 FUJITSU LIMITED

3.1 Planning Process

Copyright 2022 FUJITSU LIMITED

Section 3.1 is about the planning process.
This section explains the definition and workflow of each phase.

Copyright 2022 FUJITSU LIMITED

3.1 Planning Process - IT Vision Planning [VP] Phase -

FUJITSU

Investigate and analyze the current enterprise environment and business to define IT vision goals and measures

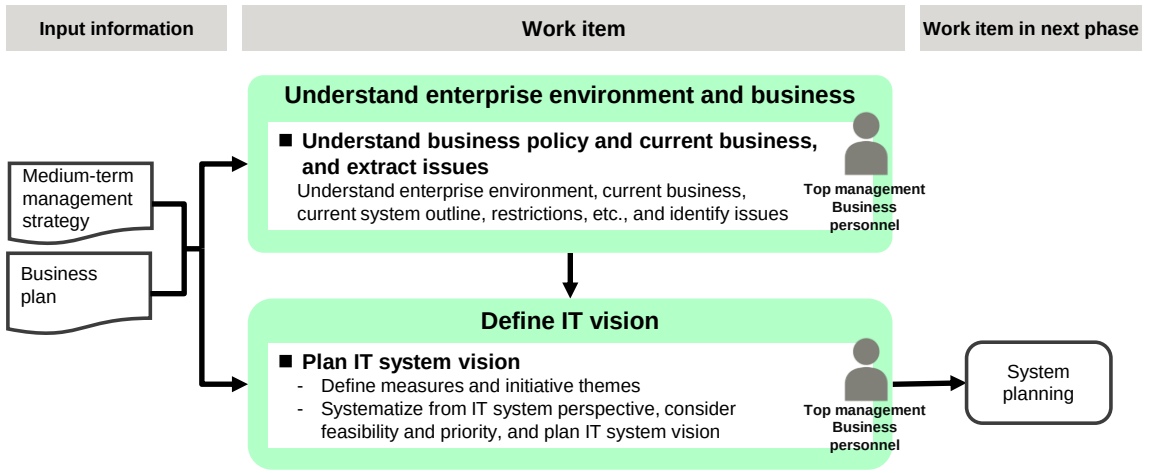

Copyright 2022 FUJITSU LIMITED

The planning process includes the VP phase and SP phase. First, here is an explanation of the IT vision planning [VP] phase.

The purposes of the VP phase are to understand the current enterprise environment and business, and to clearly define the IT vision.

The VP phase defines measures and initiative themes based on the management policy and business policy, taking current issues into account.
Then, the overall consistency, feasibility, and priority are considered from the IT system perspective and summarized as the IT system vision.

Copyright 2022 FUJITSU LIMITED

3.1 Planning Process - System Planning [SP] Phase -

FUJITSU

Based on the IT system vision, define new business requirements, estimate the ROI, and make decisions for system development

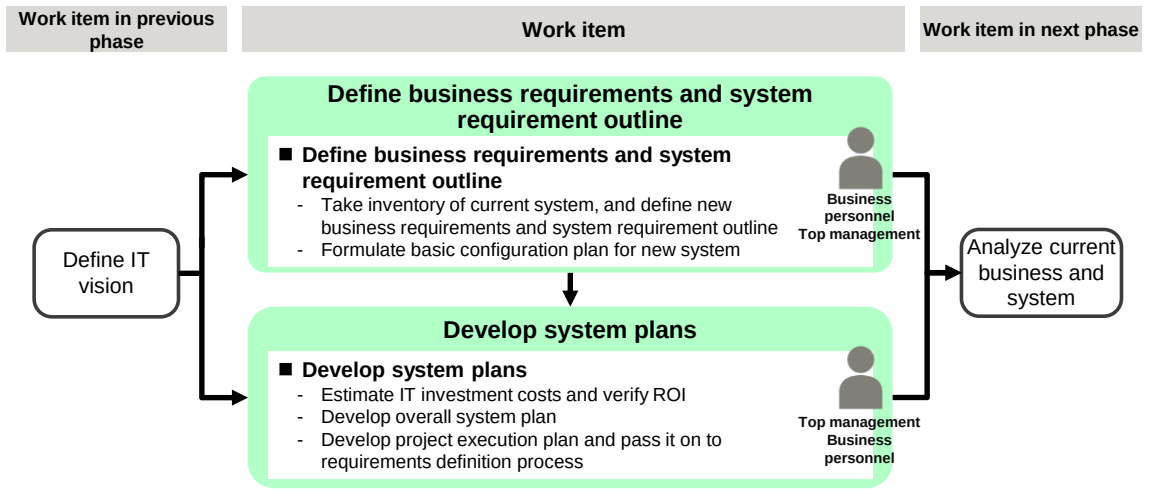

Copyright 2022 FUJITSU LIMITED

Here is an explanation of the system planning [SP] phase.

The purposes of the SP phase are to clarify what kind of system should be constructed and to define new business requirements based on the IT system vision.
Agreement on the purpose and effects of the developed system is required of the parties concerned, in consideration of the market and technology trends.

The SP phase defines new business requirements and system outline requirements, determines the overall picture of the new system, and formulates a basic configuration plan for the new system.
The costs are estimated, including the system development and operational costs of the next phase, and the ROI is verified based on the resulting estimates.
These are considered in the development of the overall system plan and project execution plan.

Copyright 2022 FUJITSU LIMITED

[Reference] Business & IT Grand Design Process Structure [BIeDP*]

FUJITSU

Systematize the work processes and knowledge for the DX vision/planning

* BIeDP:
Business & IT Enterprise Design Process

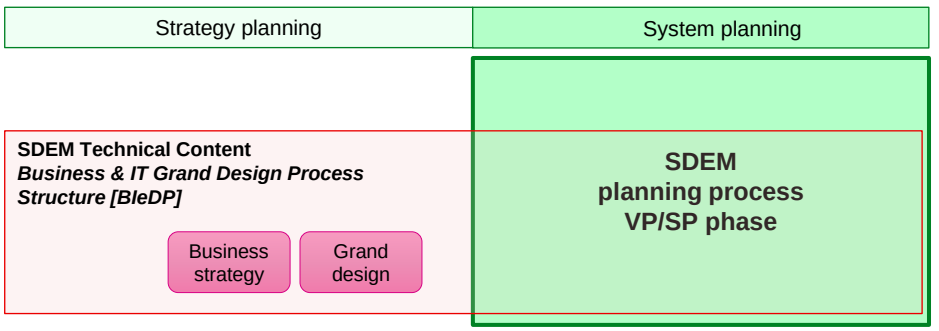

* BIeDP is included in the SDEM Technical Content. Chapter 4 introduces the SDEM Technical Content.

Copyright 2022 FUJITSU LIMITED

In business transformation utilizing the latest digital technologies, that is, DX, IT human resources familiar with digital technologies need to participate from the company-wide strategy planning and business strategy planning stages, not from the planning process.

Customers should play the main role in developing the company-wide strategy and business strategy. However, as a DX partner, we should understand the customers' ideas and provide support as an IT expert.

Business & IT Grand Design Process Structure [BIeDP] systematizes the work processes and knowledge for the DX vision/planning.
Since it is provided in the SDEM Technical Content, use it to support the customers' DX vision/planning.
Chapter 4 introduces the SDEM Technical Content.

Copyright 2022 FUJITSU LIMITED

3.2 Requirement Definition/Development/Operational Test & Transition Process

Copyright 2022 FUJITSU LIMITED

Section 3.2 explains the requirement definition process, development process, and operational test & transition process.
This section explains the roles of the categories, and then the definition and workflow of each phase.

Copyright 2022 FUJITSU LIMITED

3.2.1 Requirement Definition/Development/Operational Test & Transition Process Categories (1)

FUJITSU

Categories A and T correspond to "Overall control" and Category B corresponds to "What customers want to achieve in business."

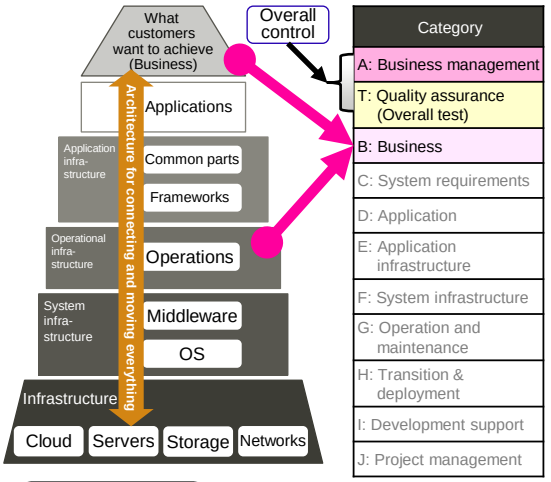

Main Category	Description	Sub Category
A: Business management	Judge the ROI, determine project startup, pause, transition, and completion, as well as organize and arrange organizations from the viewpoint of business management.	A1: Business management A2: Organization
T: Quality assurance (Overall test)	Promote overall test and manage quality for the following purposes for production: - Risk measures at project startup - Early risk measures during the project	T1: Business operation continuity judgment criteria T2: Quality assurance achievement level T3: Quality assurance scenario T4: Overall test plan and execution T5: Individual test plan
B: Business	Establish business specifications and perform business operational tests from the viewpoint of users. - Substantiate business requirements, and determine business specifications that the customer will agree with. - Design business operations, and verify the operations as business.	B1: Business operation B2: Business function B3: UX (Usage experience)

Copyright 2022 FUJITSU LIMITED

Here is an explanation of the categories.

This page is about Categories A, T, and B. Categories A and T play the role of "Overall control" in system development, and Category B corresponds to "What customers want to achieve in business."

Category A is "Business management," which is to judge the ROI, determine the project startup, pause, transition, and completion, as well as organize and arrange organizations from the viewpoint of business management.
The customer's top management is in charge of this category because it should be done from the viewpoint of business management.
The sub categories subdivided from the main categories include "Business management" and "Organization."

Category T is "Quality assurance (Overall test)," which is to promote the overall test and manage quality for the following purposes for production: risk measures at project startup, and early risk measures during the project.
It is important to work on this category with the customer and vendors as an entire project.
The sub categories are "Business operation continuity judgment criteria," "Quality assurance achievement level," "Quality assurance scenario," "Overall test plan and execution," and "Individual test plan."

Category B is "Business," which is to establish business specifications and perform business operational tests from the viewpoint of users. This category determine the specific business the customers want to achieve.
The sub categories are "Business operation," "Business function," and "UX (Usage experience)."

Copyright 2022 FUJITSU LIMITED

3.2.1 Requirement Definition/Development/Operational Test & Transition Process Categories (2)

FUJITSU

Category C corresponds to "Architecture for connecting and moving everything" and Categories D, E, and F correspond to the system structure from applications to infrastructures.

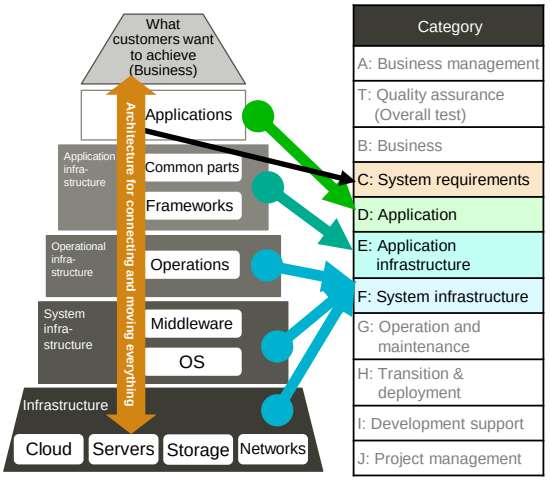

Main Category	Description	Sub Category
C: System requirements	Design the overall system architecture for doing business and then pass on that information to each category.	C1: Overall system architecture C2: Functional requirements (System functions) C3: Functional requirements (Data) C4: Functional requirements (Interface) C5: Non-functional requirements C6: Security
D: Application	Design, develop, and test applications (including packages).	D1: New application development and diversion development D2: Package usage D3: Migration (Source code conversion)
E: Application infrastructure	Design and provide common application functions deployed as a common infrastructure.	E1: Application architectures (including frameworks) E2: Database architectures and definitions (Applications) E3: Application environment
F: System infrastructure	Design and provide the system configuration and environment, network, databases, and system operations that are required for system implementation.	F1: Performance & scalability F2: Reliability F3: Security F4: External connectivity F5: System configuration & environment F6: Database F7: Network F8: Facility F9: System operation

Copyright 2022 FUJITSU LIMITED

Here is an explanation of Categories C to F. Category C corresponds to the architecture for connecting and moving everything, and Categories D, E, and F correspond to the system structure from application to infrastructure.

Category C is "System requirements," which is to design the overall system architecture for doing business and then pass on that information to each category.
The sub categories are "Overall system architecture," "Functional requirements (System functions)," "Functional requirements (Data)," "Functional requirements (Interface)," "Non-functional requirements," and "Security."

Category D is "Application," which is to design, develop, and test applications.
The sub categories are "New application development and diversion development," "Package usage," and "Migration (Source code conversion)" depending on the application development method.

Category E is "Application infrastructure," which is to design and provide common application functions deployed as a common infrastructure.
The sub categories are "Application architectures (including frameworks)," "Database architectures and definitions (Applications)," and "Application environment."

Category F is "System infrastructure," which is to design and provide the system configuration and environment, network, databases, and system operations that are required for system implementation.
Category F also includes the infrastructure, OS, middleware, and operational infrastructure.
The sub categories are classified by elements for meeting non-functional requirements. They include "Performance & scalability," "Reliability," "Security," "External connectivity," "System configuration & environment," "Database," "Network," "Facility," and "System operation."

Copyright 2022 FUJITSU LIMITED

3.2.1 Requirement Definition/Development/Operational Test & Transition Process Categories (3)

FUJITSU

Category G corresponds to "Post-production preparation" and
Categories H, I, and J correspond to "Work required in system construction/operation."

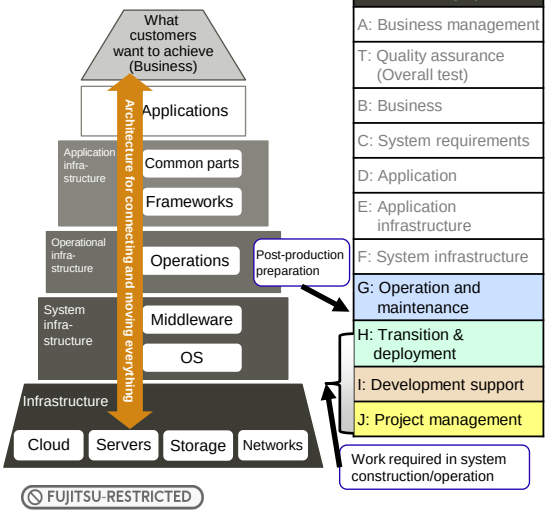

Main Category	Description	Sub Category
G: Operation and maintenance	Prepare for operation and maintenance after production (transition, etc.).	G1: Operation & maintenance
H: Transition & deployment	Plan and design transition and deployment, and perform transition rehearsal and the actual transition.	H1: Transition plan H2: Business system transition H3: Data transition H4: Deployment
I: Development support	Establish development standards for overall project integration, and develop and operate a framework for configuration management, tools, etc.	I1: Development standard I2: Configuration management
J: Project management	Develop project plans and establish project goals (deadline, quality, cost, etc.) for production, and promote and operate the project.	J1: Integration management J2: Scope management (Requirement management) J3: Time management (Progress management) J4: Cost management (Profit and loss management) J5: Quality management (Quality and defects management) J6: Human resource management (Personnel management) J7: Communications management (Information distribution and performance report) J8: Risk management (Risk control) J9: Procurement management (External procurement management) JA: Contract management (Contracts with customers) JB: OSS application management

FUJITSU-RESTRICTED

Copyright 2022 FUJITSU LIMITED

Last is Categories G to J.

Category G corresponds to "Post-production preparation." Categories H, I, and J correspond to "Work required in system construction/operation."

Category G is "Operation and maintenance," which is to prepare for operation and maintenance after production. The only sub category is "Operation & maintenance."

Category H is "Transition & deployment," which is to plan and design transition and deployment, and perform transition rehearsal and the actual transition.
The sub categories are "Transition plan," "Business system transition," "Data transition," and "Deployment."

Category I is "Development support," which is to provide support for smooth development practice, establish development standards for overall project integration, and develop and operate a framework for configuration management, tools, etc.
The sub categories are "Development standard" and "Configuration management."

Category J is "Project management," which is to develop project plans and establish goals such as deadline, quality, and cost for production, and promote and operate the project.
There are eleven sub categories in total. "Integration management," "Scope management (Requirement management)," "Time management (Progress management)," "Cost management (Profit and loss management)," "Quality management (Quality and defects management)," "Human resource management (Personnel management)," "Communications management (Information distribution and performance report)," "Risk management (Risk control)," and "Procurement management (External procurement management)" correspond to the knowledge area in the PMBOK 6th Edition. "Contract management (Contracts with customers)" and "OSS application management" are unique to SDEM.

Copyright 2022 FUJITSU LIMITED

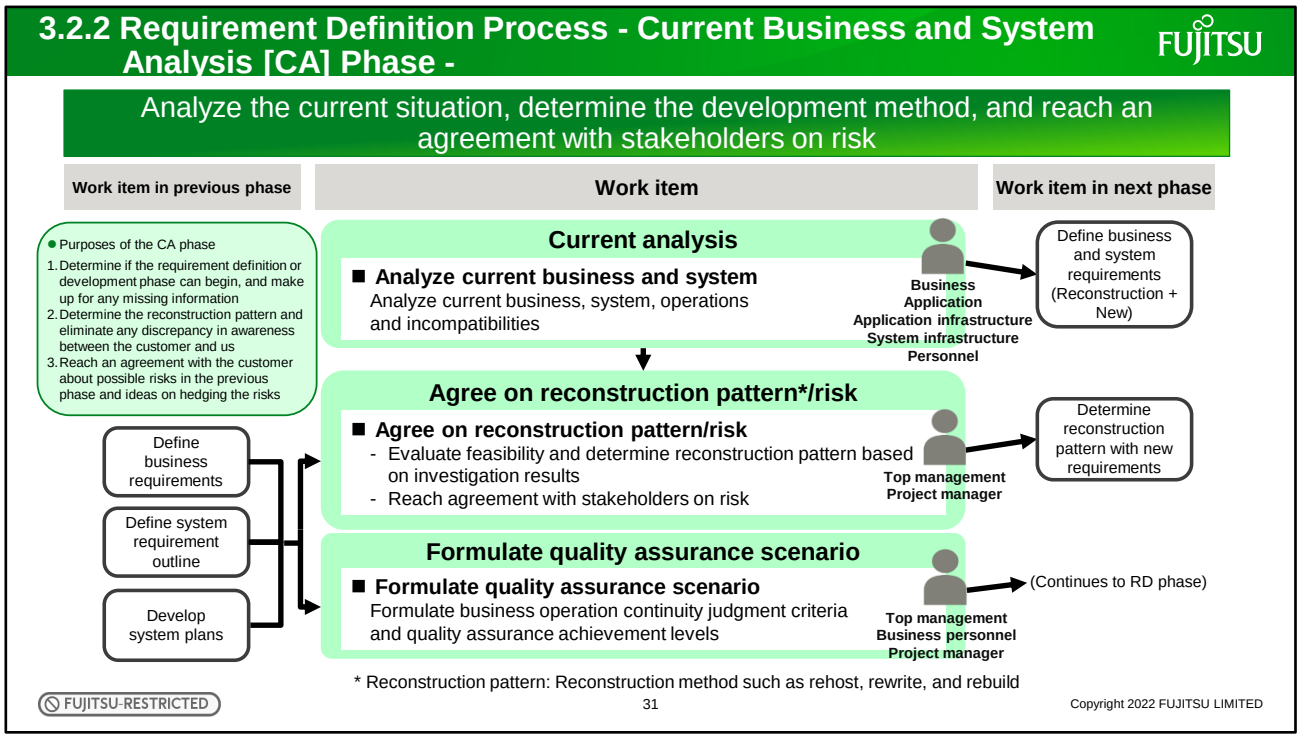

Each phase will be explained. First, the requirement definition process phase.
The requirement definition process includes the CA and RD phases. This page explains the current business and system analysis [CA] phase.

The CA phase has three purposes.
The first is to determine if the requirement definition or development phase can begin, and make up for any missing information.
The second is to determine the reconstruction pattern and eliminate any discrepancy in awareness between the customer and us.
The third is to reach an agreement with the customer on possible risks in the previous phase and ideas on hedging the risks.
In order to realize these purposes, analyze the current business, system, operations, and incompatibilities, and evaluate the feasibility and determine the reconstruction pattern based on the investigation results.
Next, reach an agreement with the customer on risk.
In addition, for quality assurance after production, formulate the business operation continuity judgment criteria and the quality assurance achievement levels.

Note that the reconstruction pattern means the reconstruction method such as rehost, rewrite, and rebuild.

Copyright 2022 FUJITSU LIMITED

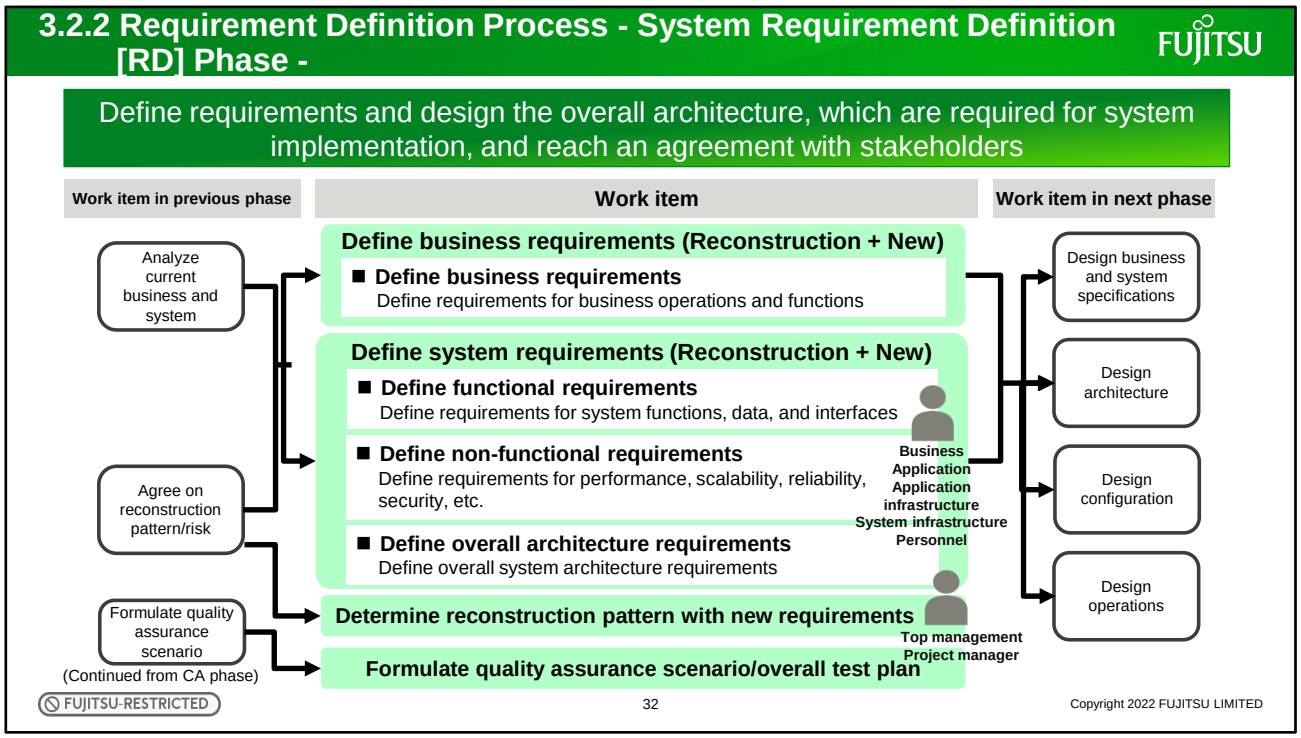

Here is an explanation of the system requirement definition [RD] phase.

The purposes of the RD phase are to define requirements and design the overall architecture, which are required for system implementation, and reach an agreement with stakeholders.

Define the requirements for business operations and functions, integrating reconstruction requirements and new requirements. System requirement definition is divided into functional requirements and non-functional requirements. The functional requirements include those for system functions, data, and interfaces. The non-functional requirements include those for performance and scalability, reliability, and security. In addition, define the requirements for the overall system architecture.
Finally, confirm the reconstruction pattern determined in the CA phase, formulate the quality assurance scenario and overall test plan, and reach an agreement with stakeholders on requirement definition.

Copyright 2022 FUJITSU LIMITED

3.2.3 Development Process - User Interface Design [UI] Phase -

FUJITSU

Design external system specifications from the user perspective, design the architecture for system implementation, and reach an agreement with stakeholders

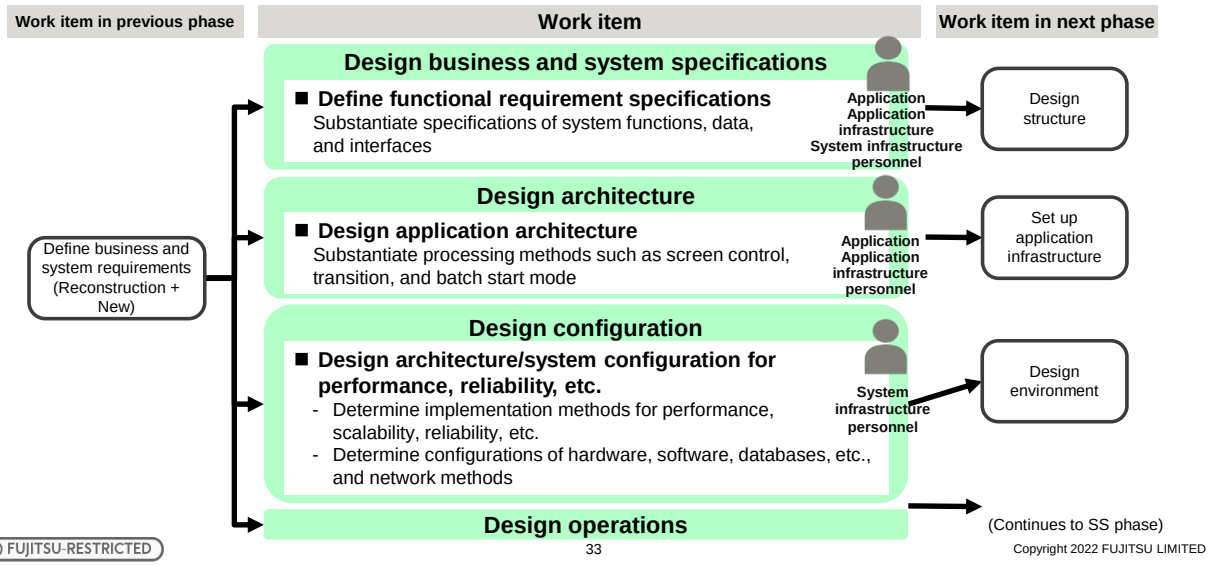

Copyright 2022 FUJITSU LIMITED

The explanations from here cover the phases of the development process. The development process includes the phases from UI to ST.
First is an explanation of the user interface design [UI] phase.

The purposes of the UI phase are to design external system specifications from the user perspective, design the architecture for system implementation, and reach an agreement with stakeholders.

In designing business and system specifications, substantiate the system functions, data, interfaces, screens, and forms based on the requirement definition of the RD phase.
In addition, design the application architecture, design an architecture for ensuring performance, reliability, etc., and determine the configurations of hardware, software, databases, etc.

Furthermore, as operation design, design the operation methods, etc. for stable, abnormal, or maintenance operations.

Copyright 2022 FUJITSU LIMITED

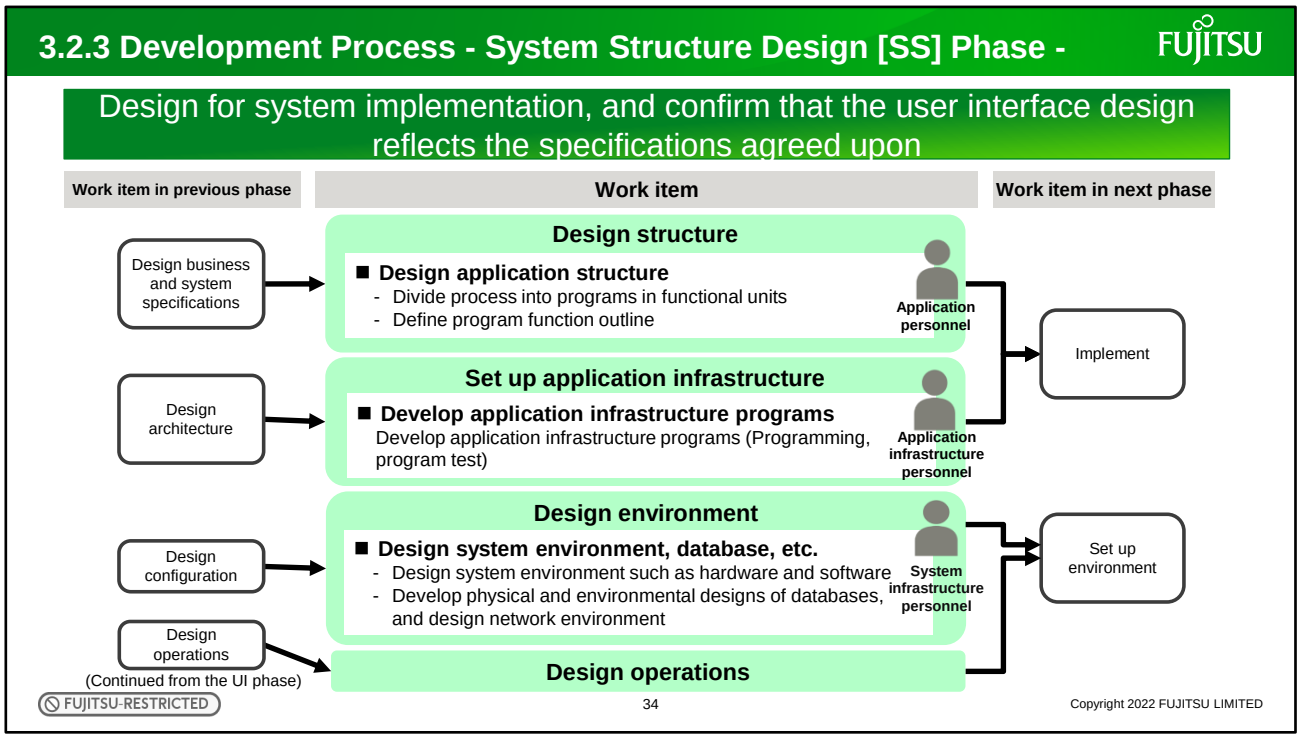

Here is an explanation of the system structure design [SS] phase.

The purpose of the SS phase is to design for system implementation.
In so doing, develop the design agreed upon with the stakeholders.

The design for implementation in this phase is based on the business and system specifications, architecture design, configuration design, and operation design in the UI phase.

In designing the application structure, define the program divisions and functions.
In setting up the application infrastructure, create application infrastructure programs one stage earlier than the start of business programming.
Then, in designing the environment, develop the environment design such as parameters related to hardware and software installed in the system, develop the physical design of the databases, and so on.

Copyright 2022 FUJITSU LIMITED

3.2.3 Development Process - Implementation Phase [PS to PT] (1) -

FUJITSU

Create programs and ensure quality by verifying them in program units

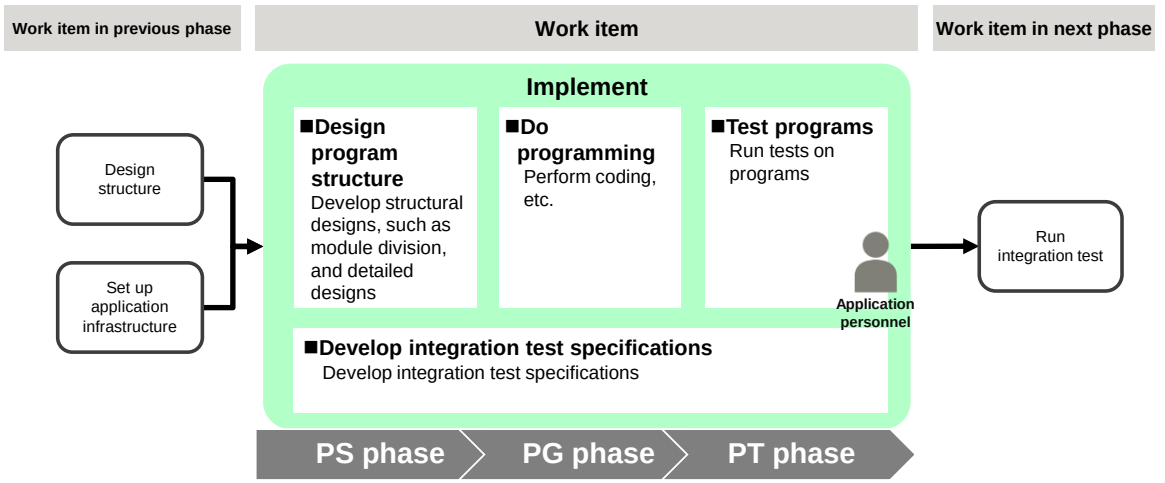

Copyright 2022 FUJITSU LIMITED

This and the next page explain the program structure design [PS] phase, programming [PG] phase, and program test [PT] phase collectively as the implementation phase.

First is an explanation of application-related work.

The PS phase develops program structure designs, such as module division, and the detailed designs of logic and algorithms to definitely incorporate the design results of the SS phase into programs.
The PG phase performs program coding.
The PT phase verifies the programs implemented in program units and ensures quality.

Copyright 2022 FUJITSU LIMITED

3.2.3 Development Process - Implementation Phase [PS to PT] (2) -

FUJITSU

Set up and verify the system infrastructure environment

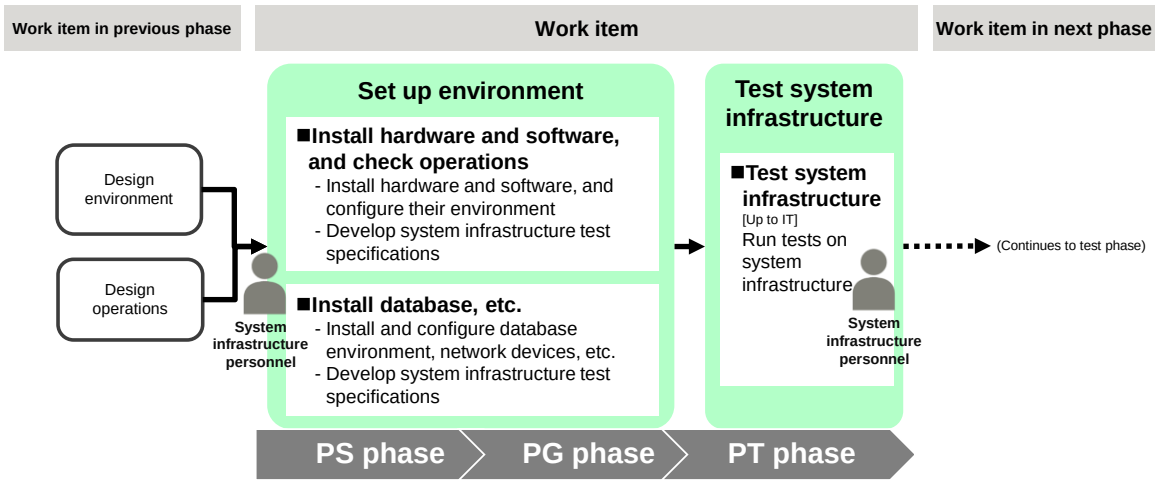

Copyright 2022 FUJITSU LIMITED

Here is an explanation of the system infrastructure work.

Set up the environment during the PS phase to PG phase.
Install hardware and software, set parameters, and install and configure the database environment, network devices, etc.
In the PT phase, test the environment that has been set up. Run the system infrastructure test by the first half of the IT phase.

Copyright 2022 FUJITSU LIMITED

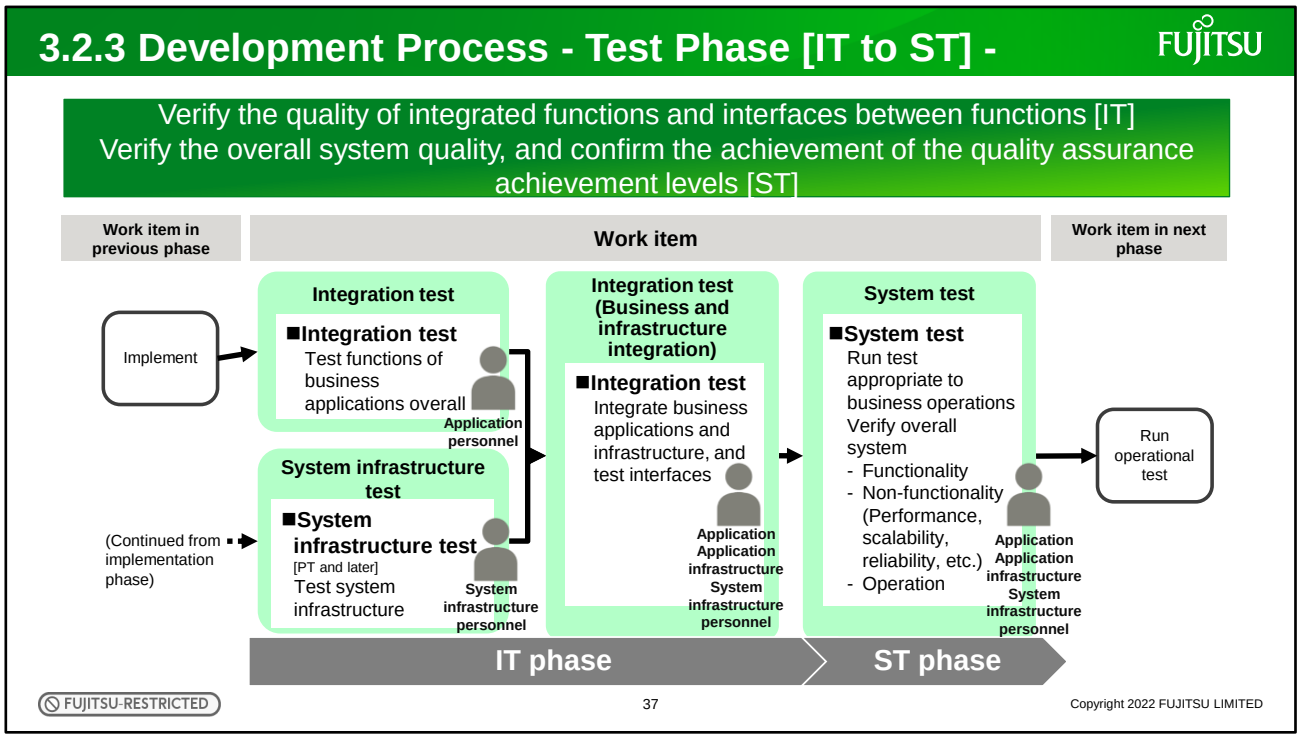

This page explains the integration test [IT] phase and system test [ST] phase collectively as the test phase.

The purposes of the IT phase are to integrate programs whose quality was confirmed in the PT phase, and to verify the quality of integrated functions and interfaces between functions.
First, run the integration test for the business applications overall.
Next, after the system infrastructure test is completed, run the integration test for the business applications on the system infrastructure. Also, verify interface quality by integrating the business and infrastructure.

The purposes of the ST phase are to verify the overall system quality and to confirm the achievement of the quality assurance achievement levels formulated together with the customer.
In the system test, verify the overall system from functional aspects, non-functional aspects such as performance and reliability, and operational aspects. For the test, use the data and system environment appropriate to the actual business operations if possible.

Copyright 2022 FUJITSU LIMITED

3.2.4 Operational Test & Transition Process - Operational Test and Transition [OT] Phase -

FUJITSU

Make production decisions based on a business scenario verification and business operation continuity judgment to transition to the new system

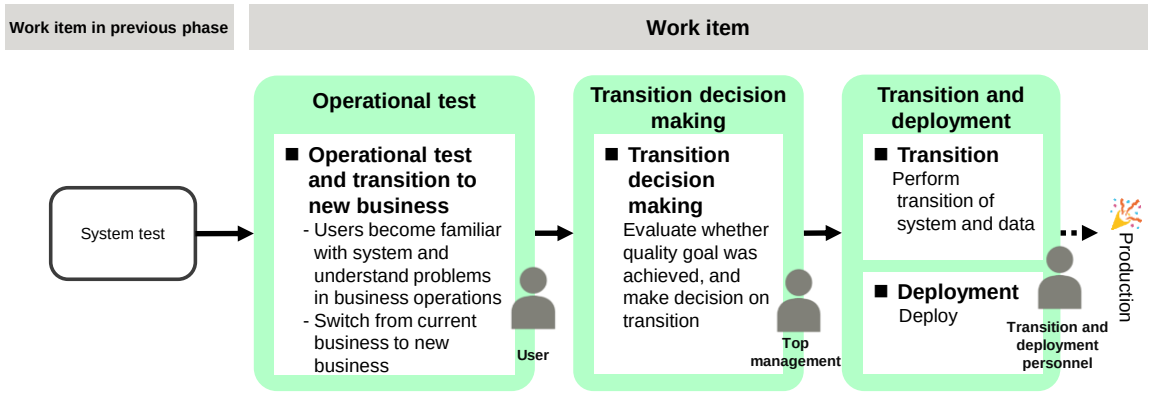

Copyright 2022 FUJITSU LIMITED

This page explains the operational test & transition process phase. The phase is operational test and transition [OT].

The purposes of the OT phase are to make a business operation continuity judgment based on business scenario verification results, etc., make production decisions based on that, and transition to the new system.

As the operational test, users verify the business scenario. Based on the business operation continuity judgment criteria and production agreed upon with the customer, determine if production is possible and if transition to the new system is possible.
When there is no problem, perform transition and deployment of the system and data.

Copyright 2022 FUJITSU LIMITED

3.2.5 Main WBS Flow of Requirement Definition/Development/Operational Test & Transition Process

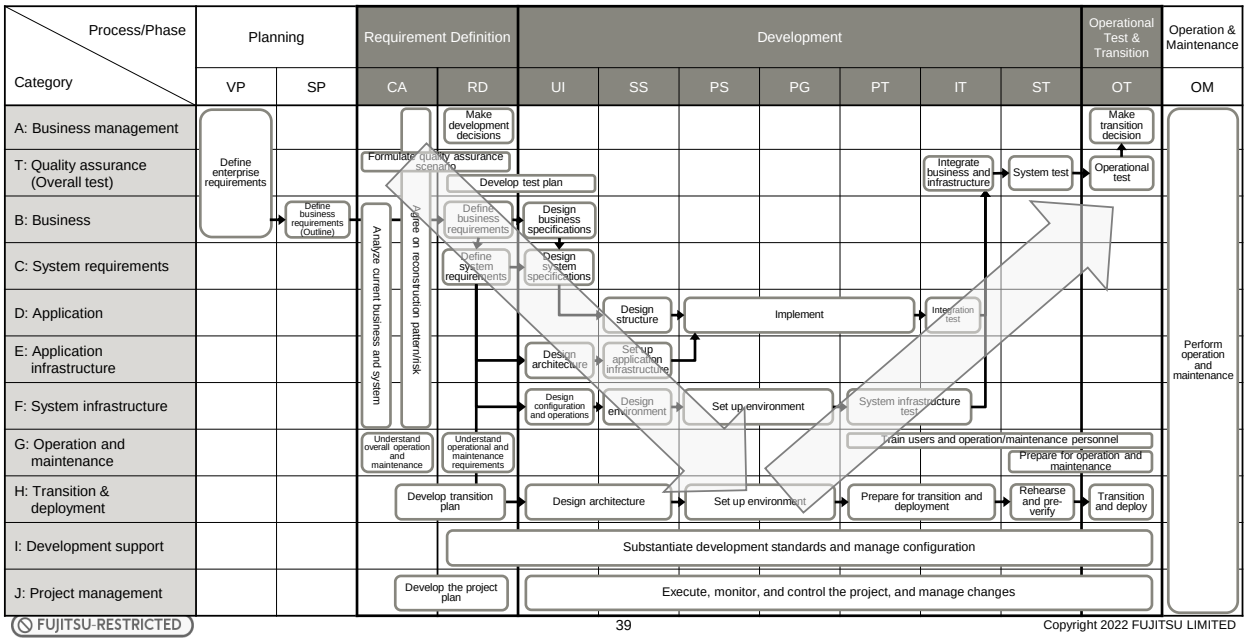

The explanations so far have covered the roles of categories of the SDEM requirement definition, development, operational test & transition processes, and the definition and workflow of each of their phases.

This diagram shows the main workflow in requirement definition, development, operational test & transition.

The explanations so far have mainly covered construction work and quality assurance. In addition to that, preparation for operation and maintenance after production, work for transition and deployment, development support, project management, and various other work have been defined.

Copyright 2022 FUJITSU LIMITED

3.3 Operation & Maintenance Process

Copyright 2022 FUJITSU LIMITED

Section 3.3 explains the operation & maintenance process.

Copyright 2022 FUJITSU LIMITED

3.3 Operation & Maintenance Process - Operation and Maintenance [OM] Phase -

FUJITSU

Develop a plan for safe and stable operation of the IT system, and regularly review and improve the plan

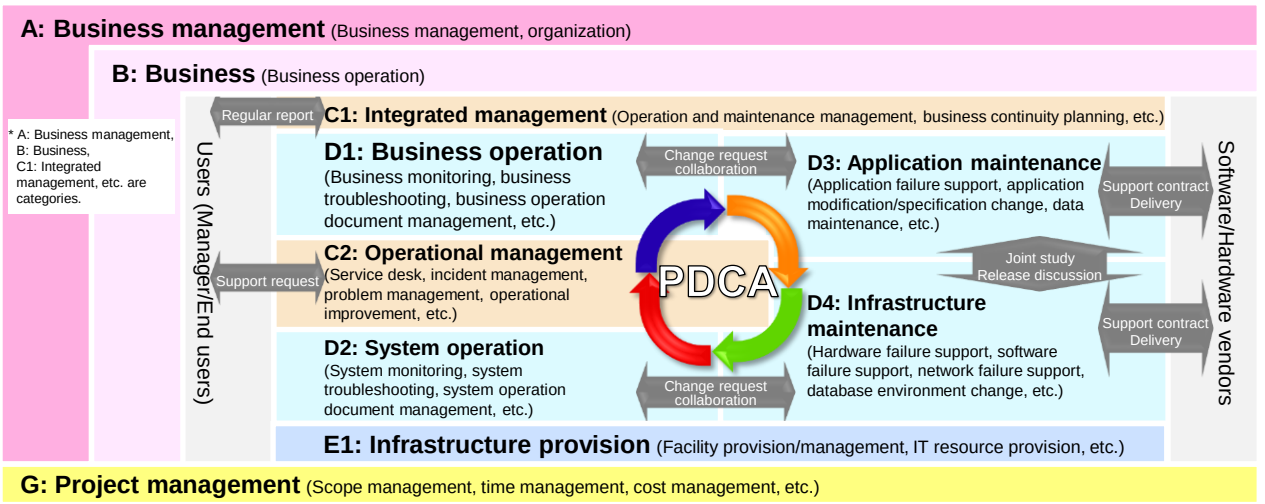

Copyright 2022 FUJITSU LIMITED

The operation & maintenance process includes only the operation and maintenance [OM] phase because it has no concept of start and end like in a development project.

In the OM phase, develop a plan for safe and stable operation of the system, and regularly review and improve the plan cyclically.
For daily operation and maintenance, go through a cycle centered on operation management, from business operation, system operation, application maintenance, and infrastructure maintenance request to delivery.
Engage in integrated management from the perspective of management and business.

Copyright 2022 FUJITSU LIMITED

4. SDEM 2.0 Content Structure

What you will understand by the end of this chapter

- What kind of content is provided with SDEM
- Types of SDEM practical standards, and what is provided

Copyright 2022 FUJITSU LIMITED

Chapter 4 explains the SDEM content structure.
By the end of this chapter, you will understand the content provided with SDEM, types of SDEM practical standards, which are part of it, and what is provided.

Copyright 2022 FUJITSU LIMITED

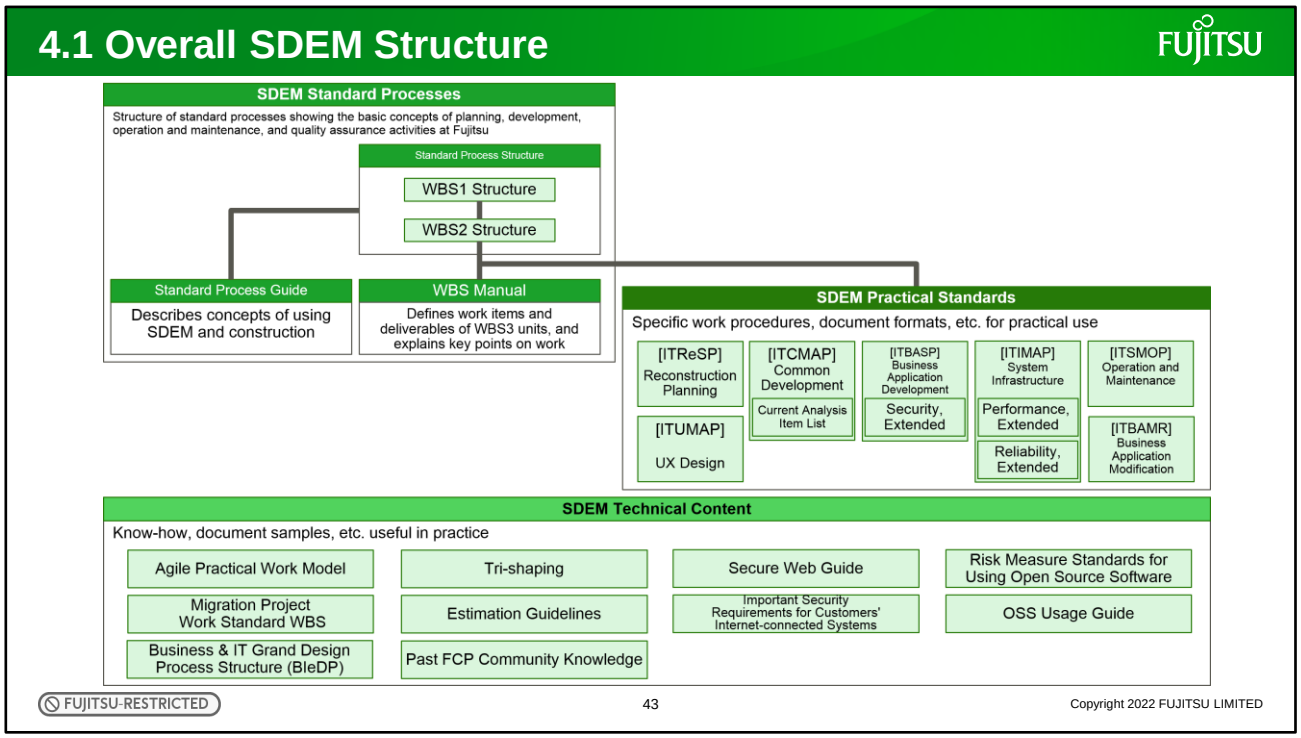

SDEM broadly consists of the SDEM Standard Processes, the SDEM Practical Standards, and the SDEM Technical Content.

The SDEM Standard Processes are a general-purpose work structure independent of industry, language, development environment, and so on. It covers the overall work required for planning, development, operation and maintenance, and quality assurance activities.
They contain three types of content: *Standard Process Structure*, *WBS Manual*, and *Standard Process Guide*.

The SDEM Practical Standards are provided as more practical work standards for each field.
Document formats, samples, specific work procedures, and guides are provided.

The SDEM Technical Content contains technical know-how and document samples useful in practicing Fujitsu project work.

Starting with the next page, the content provided in the SDEM Standard Processes is introduced.

Copyright 2022 FUJITSU LIMITED

4.2 SDEM Standard Processes - Standard Process Structure -

FUJITSU

- SDEM (WBS1-2 structure) key point summary

Use for project planning (estimation, schedule creation, role division), etc.

[Planning, requirement definition, development, operational test & transition, operation & maintenance process WBS1]

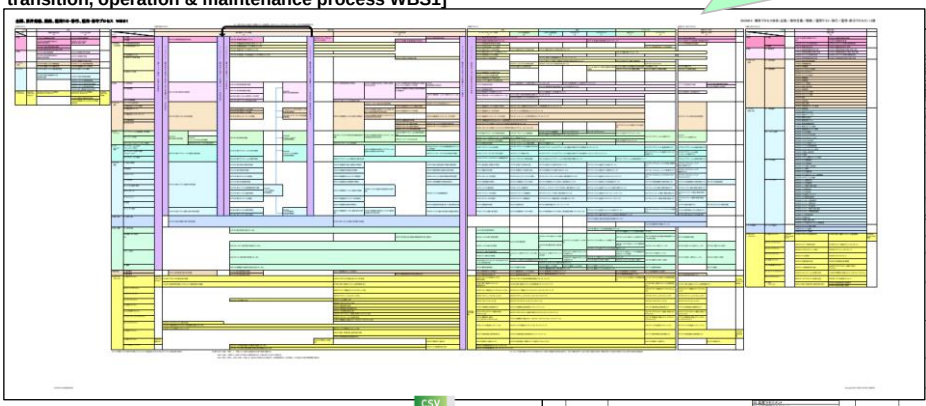

[Explanation of categories and phases]

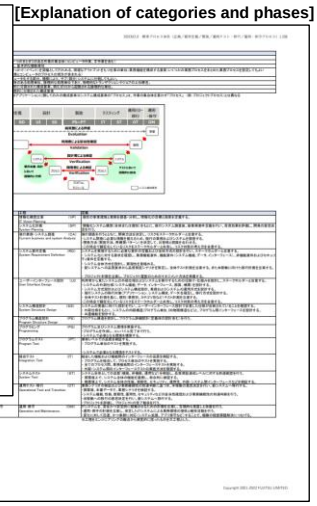

- WBS1-2 provided
- Printable (A3) files also provided
- WBS data in CSV format also provided (WBS1-2-3)

Use to:
- Collect detailed tasks
- Extract the WBS name in schedule creation

Copyright 2022 FUJITSU LIMITED

First is an explanation of the *Standard Process Structure*.

This content includes the WBS1 and WBS2 structures, categories, and phase definitions of the SDEM standard processes.
Take advantage of the content to get an overall picture of the SDEM standard processes.
When estimating project work and planning role division, be sure to use this standard process structure.

In addition, WBS1, WBS2, and WBS3 lists are provided in CSV format. Use them for project standardization, WBS name extraction in schedule creation, etc.

Copyright 2022 FUJITSU LIMITED

4.2 SDEM Standard Processes - WBS Manual -

FUJITSU

- Explanation of key points of work in each WBS

SDEM2.0 WBS説明書

工程	大カテゴリ	小カテゴリ
RD：システム要件定義	B：業務	B2：業務機能

ＷＢＳ第１レベル	B2RD100	新規業務要件の明確化
ＷＢＳ第２レベル	B2RD110	新規要件（業務機能）の洗い出しと明確化

入力ファイル	―	ＲＦＰ、企画書
	Z1CA500f1	再構築方針書（要求事項一覧）
	B1CA100f1	現行調査結果（システム化業務フロー、業務関連図、業務一覧、新システム移行対象ファイル一覧）

出力ファイル	B2RD200f1	業務要件定義書（新規要件）

ＷＢＳ第３レベル		出力ドキュメント	
1	新規及び変更要件（業務プロセス機能）の洗い出し	d1	システム化業務フロー（新規要件の朱書きイメージ）
2	新規及び変更業務プロセスの機能要件の明確化	d1	業務関連図（新規要件の朱書き）
		d2	業務一覧（新規要件）
3	業務処理量の見積り	d1	業務処理量一覧（新規要件）

作業のポイント

＜共通＞

【目的】新規及び変更する業務の機能要件を洗い出し、明確化する。

1. 新規及び変更要件（業務プロセス機能）の洗い出し

ＲＦＰ・企画書、要求事項一覧及びシステム化業務フローから、新たに追加及び変更する業務プロセスを洗い出し、機能要件を明確化する。

＜業務機能要件の検討観点＞

①新規業務からの新たな機能要件

- Provided in WBS2 units
- Describes the WBS purpose and input/output
- Describes key points of work and viewpoints for consideration for WBS3 individually

* The *WBS Manual* is not provided for Categories C to E in the operation & maintenance process (OM).
See the *SDEM Practical Standards: Operation and Maintenance (ITSMOP)*.

Use to:
- Understand the procedure and viewpoints of work you are in charge of
- Get reviewers and auditors to check if they missed some checks

Copyright 2022 FUJITSU LIMITED

Next is about the *WBS Manual* in the SDEM Standard Processes.

This content is provided in WBS2 units.
It shows what to input or output in each WBS, and the key points of work and viewpoints for consideration for WBS3 individually.
Use it to understand work you are experiencing for the first time, and so on.

This content also includes the WBS purpose.
When performing work, it is important to understand the purpose of the work.
When reading the *WBS Manual*, pay attention to this purpose to deepen your understanding.

Copyright 2022 FUJITSU LIMITED

4.2 SDEM Standard Processes - Standard Process Guide -

FUJITSU

- Explains SDEM concepts and application methods * Table of contents is below

Purpose of SDEM® 2.0 Renewal

Chapter 1 What is SDEM?
- 1.1 Need for Standardization
- 1.2 Fujitsu Standardization
- 1.3 Incorporation of Global/De Facto Standards
- 1.4 History of Standardization at Fujitsu

Chapter 2 SDEM Structure
- 2.1 Processes
- 2.2 Categories
- 2.3 Phases

Chapter 3 Planning Process
- 3.1 Overall Flow
- 3.2 Categories
- 3.3 Phases

Chapter 4 Requirement Definition/Development/ Operational Test & Transition Process [For internal use]
- 4.1 Overall Flow
- 4.2 Categories
- 4.3 Phases

Chapter 5 Operation & Maintenance Process
- 5.1 Overall Flow
- 5.2 Categories
- 5.3 Phases

Chapter 6 Contract/Organizational Management/System Audit Process
- 6.1 Contract Process
- 6.2 Organizational Management Process
- 6.3 System Audit Process

Chapter 7 Applying SDEM

Chapter 8 System Development Concepts Where "It is Natural for Existing Systems to Exist"
- 8.1 Concept of New Development
- 8.2 Concept of Reconstruction

Conclusion

Appendix 1. File Structure
Appendix 2. Main Workflow of Requirement Definition Process (CA to RD Phases)
Appendix 3. Reconstruction Pattern
Appendix 4. Relationship Between Global/De Facto Standards and SDEM
Appendix 5. Details of SDEM 2.0 Changes [For internal use]

Use if you:
- want to understand SDEM in more detail than provided in this training course
- are a project manager who wants to understand key points within the company to proceed smoothly with projects

* Parts of Chapter 4 and Appendix 5 are confidential information.
Therefore, the confidential information has been from the *Standard Process Guide* (FUJITSU-CONFIDENTIAL version) used by customers and partners.

Copyright 2022 FUJITSU LIMITED

The third type of content in the SDEM Standard Processes is the *Standard Process Guide*.
This page shows the table of contents of the guide.

This content explains each SDEM process and the concepts of SDEM application methods.

The *Standard Process Guide* has been divided into an internal version and the FUJITSU-CONFIDENTIAL version. The internal version explains the key points to progressing smoothly in a project.
Read it if you want to understand these points or want to understand SDEM in more detail than provided in this training course.

These pages have explained the *Standard Process Structure*, *WBS Manual*, and *Standard Process Guide* in the SDEM Standard Processes.
Next is an explanation of the SDEM Practical Standards.

Copyright 2022 FUJITSU LIMITED

4.3 Structure of SDEM Practical Standards

FUJITSU

The SDEM Practical Standards provides specific work procedures, document formats, etc. in practice.

Use to:
- Understand practical know-how about work you are in charge of
- Determine the document standards for a project

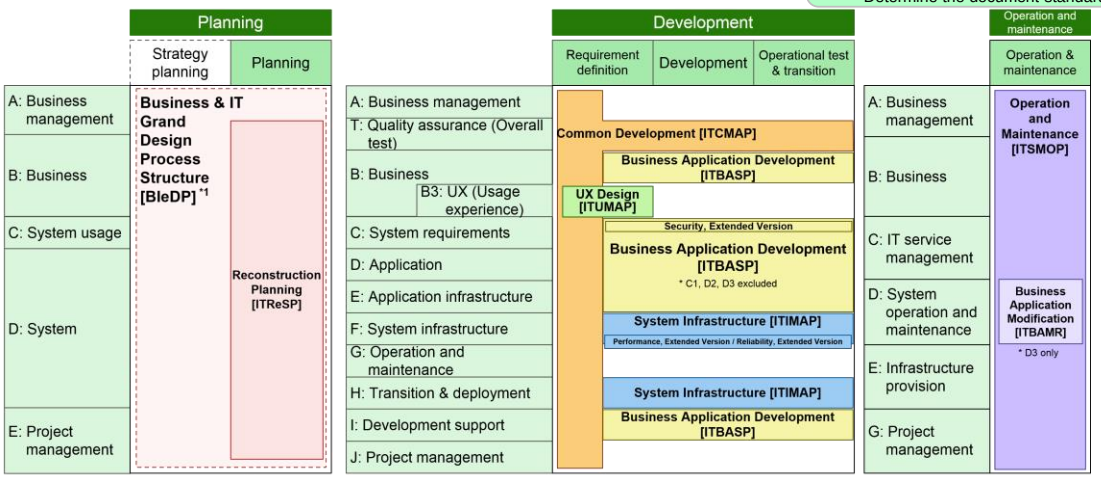

*1 The *Business & IT Grand Design Process Structure (BleDP)* is available in the SDEM Technical Content.

* For the location of document formats and samples, including the *SDEM Practical Standards*, see "ドキュメントフォーマット・サンプル格納場所" (Document format/sample storage location) on the following page:
https://fujitsu.sharepoint.com/sites/jp-IKB-sdem/SitePages/technology/sdeminformation.aspx

Copyright 2022 FUJITSU LIMITED

The SDEM Practical Standards provide more practical procedures and guides, document formats and samples, etc., such as Business Application Development and System Infrastructure for each process and category.

Use it to understand practical know-how about work you are in charge of or to determine the document standards for a project.

Copyright 2022 FUJITSU LIMITED

FUJITSU

5. Applying SDEM

What you will understand by the end of this chapter

- Concept of applying SDEM to projects
- Concept and important points of tailoring
- Concept of utilizing SDEM in agile development

Copyright 2022 FUJITSU LIMITED

Chapter 5 explains how to apply SDEM to projects.
By the end of this chapter, you will understand the concept of applying SDEM to projects, the concept and important points of tailoring, and the concept of utilizing SDEM in agile development.

Copyright 2022 FUJITSU LIMITED

5.1 Applying SDEM to Projects

FUJITSU

Tailor and utilize according to project characteristics.

SDEM is a comprehensive structure of work to be done in system construction. SDEM is not premised on a specific application (scale or system form) or implementation means (process model, technique, tool).

Therefore, to apply it to an actual project, **tailor** (customize the depth of) and utilize **the WBS implementation** according to the project characteristics.

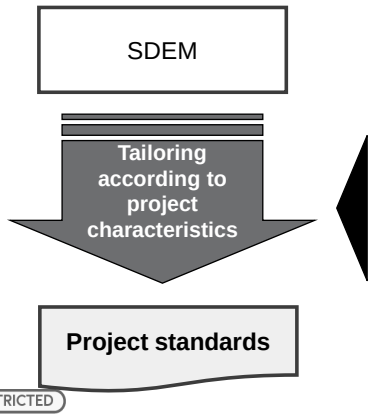

[Viewpoint of tailoring]

Project Characteristics		
System Characteristics	**Technical Conditions**	**Development Conditions**
- Scale - Application type - Core system/Information system - Quality requirements etc.	- Development model (Waterfall, agile, etc.) - New development, reconstruction, service application - Methods/Tools etc.	- Development period - Skills/Scheme - Development form etc.

Copyright 2022 FUJITSU LIMITED

The first is the concept of applying SDEM to projects.

SDEM is a comprehensive structure of work to be done in system construction. SDEM is not premised on a specific product, system form, or implementation means.
Therefore, to apply it to an actual project, tailoring according to the project characteristics is necessary.

"Tailoring" means to customize the depth of WBS implementation according to project characteristics.

The viewpoints of tailoring include system characteristics, such as the scale and application type, and conditions such as the development model, new development or reconstruction, skill level, and development form.

Copyright 2022 FUJITSU LIMITED

5.2 Concept of Tailoring

FUJITSU

- WBS tailoring

Tailoring is implemented based on the following concepts.

WBS1	Basically covers the implementation of all WBS
WBS2	Basically covers the implementation of all WBS
WBS3	Selects the WBS to be implemented according to project characteristics Determines the depth of work to be done

- Integrate and divide phases

Point 1. Do not integrate phases of different processes

As an example, do not integrate the RD phase of the requirement definition process and the UI phase of the development process, or the ST phase of the development process and the OT phase of the operational test & transition process. The purposes of the phases are different. Make sure the phases are independent of each other regardless of the period length.

Point 2. Divide a phase

If a phase has many system components (business, sub system, etc.) due to the project characteristics, divide the phase.

When dividing a phase and defining the sub phases, make it clear that the purpose of the original phase can be achieved, and clarify the purpose and outline of each sub phase along with its name.

[Example of dividing the IT phase]

IT1 (Inter-program integration test within process), IT2 (Inter-process integration test), IT3 (Interface test with external system)

Copyright 2022 FUJITSU LIMITED

Here is an explanation of the concept of tailoring.

In many cases, you will refer to similar projects in the past to determine the project standards. The benefits this will bring include a greater awareness of additional work due to project characteristics or optimization of the formulation of the project standards. On the other hand, there is a risk that the work required for this project will be omitted. Therefore, while referring to past projects, start tailoring based on all WBS of SDEM.

Especially for WBS1 and 2 level work, consider implementing every WBS once.
When deciding against implementation, it is important to be able to explain to a third party why the project requirements can be met without the implementation. An example of a reason is that they are clearly not applicable depending on the project scope.
A careless decision will lead to quality problems.
Depending on the development framework and applied language, for example, you may need to make a choice or review the work at the WBS3 level.

There are special points to keep in mind when integrating or dividing a phase.

For example, depending on the project, the PS and PG phases are integrated in many cases.
However, as an example, do not integrate the RD phase of the requirement definition process and the UI phase of the development process, or the ST phase of the development process and the OT phase of the operational test & transition process.
The purposes of the phases differ greatly, so it is essential to judge the completion of each phase.

Conversely, it may be better to divide a phase.
For example, by dividing the IT phase into IT1, IT2, and IT3 depending on the scope of integration, you can clarify the purpose to be achieved in each of them, and manage the quality, progress, etc. in divisions.

Copyright 2022 FUJITSU LIMITED

5.3 Concept of Utilizing SDEM in Agile Development

FUJITSU

The work and examination viewpoints defined in the SDEM WBS are the elements required for system development.
Ascertain and utilize the required elements according to the purpose of development.

Agile development

Agile development has no concept of dividing a phase. The actions in each short development cycle are requirement definition, design, implementation, and testing. Check requests and repeat implementation in the short cycle to continuously create value.



Copyright 2022 FUJITSU LIMITED

This chapter ends with an explanation of how to use SDEM in agile development.

Agile development has no concept of dividing a phase. However, the fact remains that requirement definition, design, implementation, and testing are agile actions.

The work and examination viewpoints defined in the SDEM WBS are the elements required for system development.
Ascertain and utilize the required elements flexibly according to the purpose of development in the project.

Copyright 2022 FUJITSU LIMITED

FUJITSU

6. SDEM Usage Scenarios

What you will understand by the end of this chapter

- When to use SDEM
- What can be done with SDEM
- How far the SDEM provision scope extends
- Where to obtain SDEM, and contact information

Copyright 2022 FUJITSU LIMITED

Chapter 6 explains specific SDEM usage scenarios.
By the end of this chapter, you will understand when to use SDEM, what can be done with SDEM, how far the SDEM provision scope extends, and where to obtain SDEM.

Copyright 2022 FUJITSU LIMITED

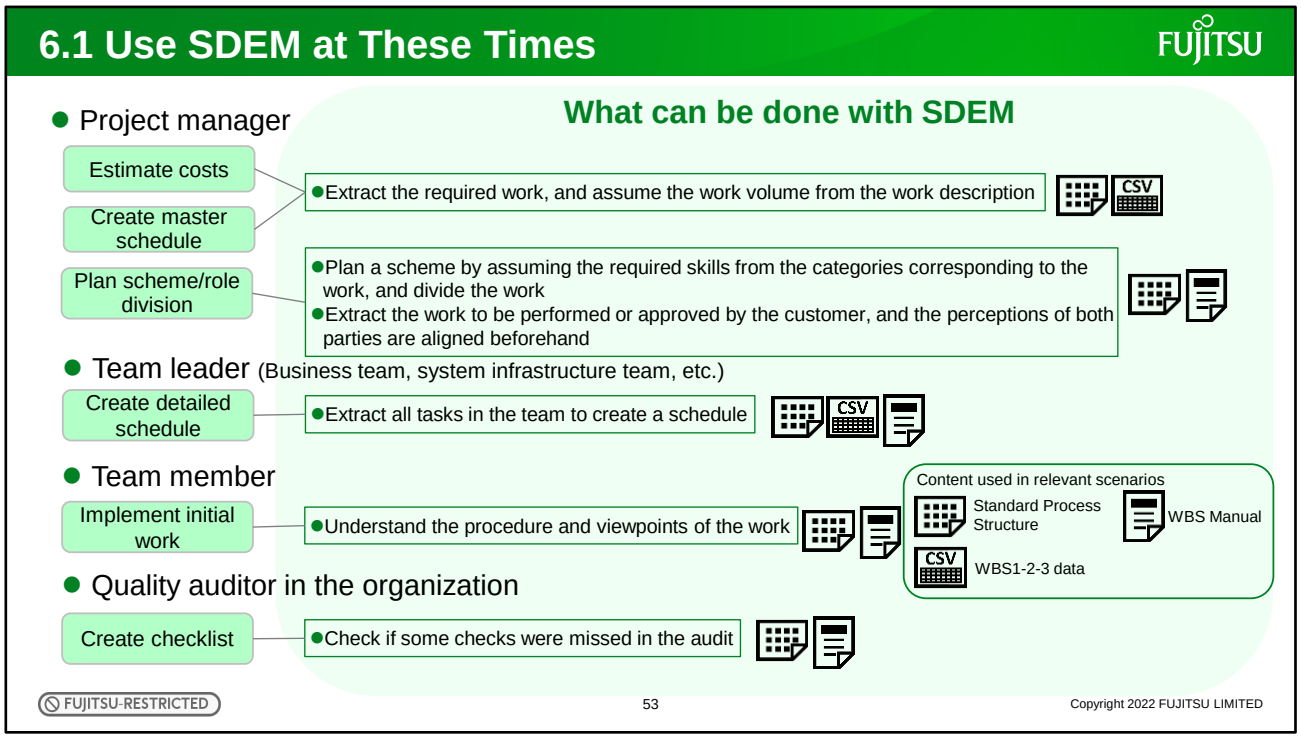

Here is an explanation of the typical usage scenarios of SDEM for each role.
The icons on the right represent the content mainly used in the scenario.

A project manager can use SDEM to estimate costs, create a master schedule, and plan a scheme and role division.
All required work, including that related to the customer, can be extracted. This can be used not only for planning Fujitsu's work but also for planning work where you need to share a common perception with the customer early.
The next page explains an image of planning a scheme and role division using SDEM categories.

The leader of a business team, infrastructure team, or subsystem team can extract all the work in the team by referring to specific WBS work to create a detailed schedule.

Team members will understand the procedure and viewpoints of the work even when experiencing the work for the first time. They will also understand the positioning of their work in the overall work.

SDEM can be used not only in a project but also by quality auditors in the organization.
The auditors can check if they missed some checks on a checklist used in the audit.

Copyright 2022 FUJITSU LIMITED

6.2 SDEM Usage Scenario 1) Planning Project Plan Scheme and Role Division

FUJITSU

Use SDEM categories to clarify the targets (application, infrastructure, etc.) and define roles for each group in the project.
Confirm that all elements in the category are assigned in order to prevent omissions and gaps in role division.

[Example of development scheme planning]

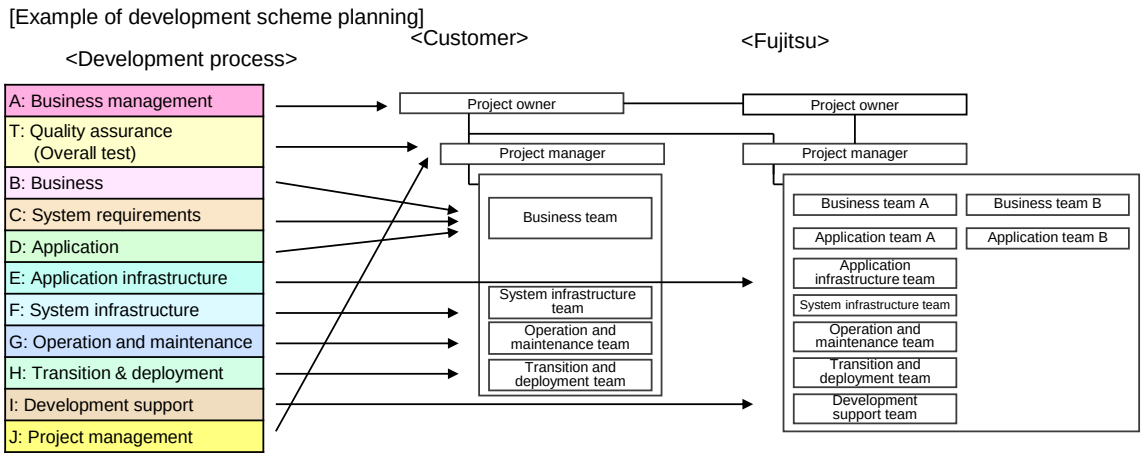

Copyright 2022 FUJITSU LIMITED

Here is an explanation of an image of specific usage.
The figure on this page is an image showing SDEM usage for planning a project scheme and role division.

The SDEM categories are classified based on the relevance of knowledge and skills required for work. The categories are used to clarify the targets such as application, infrastructure, and operations, and to define the scheme and roles of the project.

As shown in the figure, confirm that all elements in the category, including the customer's scheme, are assigned in order to prevent omissions and gaps in role division.

Copyright 2022 FUJITSU LIMITED

6.3 SDEM Usage Scenario 2) Creating Schedule

FUJITSU

Define the project WBS based on the SDEM WBS, and create work items/schedules.





Collect required work items

Collected Work Items
C4UI111 Screen transition design
C4UI112 Screen layout design
C4UI113 Screen item design
C4UI141 Collection of common business messages

Assign deliverables and personnel

[New system project] Person-hour estimates/role division/schedule

Work Item	Document	Person-hours	Personnel	Schedule
Screen transition design	Screen transition diagram	10	A	
Screen layout design	Screen layout	7	B	
Screen item design	Screen item definition	15	B	
Collection of common business messages	Business message list	30	C	

FUJITSU-RESTRICTED

55

Copyright 2022 FUJITSU LIMITED

Here is an explanation of another image of specific usage. This page explains a usage scenario for creating a schedule.

First, extract the work and output required for the project from the SDEM WBS to create a schedule.
Then, you can assign and schedule all the deliverables you need to create.

Copyright 2022 FUJITSU LIMITED

6.4 Scope of SDEM 2.0 Provision

FUJITSU

SDEM is Fujitsu's core technology and important know-how for Fujitsu to outsource SI.
Therefore, provision to an external party is based on the premise that an NDA is concluded and Fujitsu is entrusted with SI.

SDEM is copyrighted by Fujitsu, and the scope of provision varies depending on the content.

SDEM Structure		Internal Provision Scope	External Provision Scope	
		Within Company/Group	Business Partner	Customer
SDEM Standard Processes	Standard Process Structure	✓	◆	◆
	WBS Manual	✓	◆	◆
	Standard Process Guide (FUJITSU-CONFIDENTIAL)	✓	◆	◆
	Standard Process Guide (for internal use)	✓	x	x
	WBS1-2-3 work item list (CSV format)	✓	x	x

[Legend]
✓: Can be provided
◆: Can be provided after the conclusion of a non-disclosure agreement (NDA), representing a confidentiality agreement, on the premise that Fujitsu is entrusted with SI
x: Cannot be provided or shown

* For the provision scope of the SDEM Practical Standards, see "利用上の注意事項" (Precautions for Use) on the following page:
https://fujitsu.sharepoint.com/sites/jp-IKB-sdem/SitePages/technology/attention.aspx

Copyright 2022 FUJITSU LIMITED

Here is an explanation of the scope of provision of SDEM 2.0.
SDEM is Fujitsu's core technology and important know-how for Fujitsu to outsource SI.
Therefore, provision to a customer or business partner is based on the premise that Fujitsu is entrusted with SI.
In addition, a non-disclosure agreement, representing a confidentiality agreement, must be concluded.
As shown in the table, some content cannot be provided outside the company.

Furthermore, the scope of provision of the SDEM Practical Standards is determined by content.
When using it, check "利用上の注意事項" (Precautions for Use) on the IKB site.

Copyright 2022 FUJITSU LIMITED

6.5 SDEM 2.0 Published by IKB-SDEM

FUJITSU

- A variety of information such as introductory materials and the content introduced in this training course is available on the IKB-SDEM site.
  (IKB-SDEM site) https://fujitsu.sharepoint.com/sites/jp-IKB-sdem/SitePages/sdem.aspx

* English versions of the following content are also available:
- *SDEM Standard Processes: Standard Process Structure*
- *SDEM Practical Standards: Operation and Maintenance [ITSMOP]*

- For inquiries, please contact us from [Inquiry] on the menu on the IKB-SDEM site.

Copyright 2022 FUJITSU LIMITED

The SDEM content introduced in this training course and the textbooks for this training can be obtained from the IKB-SDEM site. Please make use of them.
For inquiries, please contact us from [Inquiry] on the menu.

The standard process structure "SDEM" is available to provide a system that our customers can use with peace of mind. SDEM is the culmination of Fujitsu SE's wisdom and covers all system development tasks, including the customer ones.
Please use SDEM to work with good quality and without omission.

Copyright 2022 FUJITSU LIMITED

Thank you

Copyright 2022 FUJITSU LIMITED
